

# DAM REHABILITATION AND IMPROVEMENT PROJECT DRIP PHASE II(Funded by World Bank)

## KODAYAR DAM-I

**TN12HH0053**

## ENVIRONMENT AND SOCIAL MANAGEMENT PLAN (ESMP)



**FEBRUARY 2025**

**Tamil Nadu Green Energy Corporation Limited (TNGECL)**



### **IMPORTANT NOTE**

This ESMP is prepared with management plans for all relevant ESSs.

Dam specific inputs and Management Plans of Kodayar dam- I and Tribal Development Plan of Kodayar dam- I are used in this ESMP purely for guidance purposes.

This ESMP shall be updated with sub-project specific data/ ESDD outcomes/management plans as identified in ESDD for preparing sub-project Dam specific ESMP, as applicable.



## Table of Contents

### **Appendix 1: Standard Environmental And Social Management Plan (ESMP)**

#### **Chapter 1: Project Overview And Findings Of ESDD.**

1.1. Project Overview .....	1
1.2. Objective And Context Of ESMP .....	2
1.3. Sub Project Description.....	3
1.4. Proposed Interventions/ Activities And Intended Outcomes.....	4
1.5. Esdd Findings And Key Impacts To Be Addressed.....	7

#### **Chapter 2: Environmental And Social Management Plans.....9**

2.1 Gender Based Violence Or Sea/Sh Related Actions (ESS1).....	9
2.2 Labor Management Procedure (ESS2).....	10
2.2.1 Overview Of Labor Use In The Project .....	10
2.2.2 Assessment Of Key Potential Risks .....	10
2.2.3 Responsible Staff .....	11
2.2.4 Policies And Procedures.....	11
2.2.5 Age Of Employment .....	14
2.2.6 Terms And Conditions.....	14
2.2.7 Grievance Mechanism .....	15
2.2.8 Contractor Management .....	15
2.3 Resource Efficiency And Pollution Prevention (ESS3).....	16
2.3.1 Pollution Prevention And Environment Quality Management Plan (PPEQMP).....	16
2.3.2 Overview Of PPEQMP .....	19
2.3.3 How Water And Other Resource Use Will Be Planned .....	20
2.3.4 Environmental Quality Monitoring Plan And Protocols .....	20
2.3.5 Reporting .....	21
2.4 Community Health And Safety (ESS4) .....	21
2.4.1 Overview.....	21
2.4.2 Hazard Identification .....	21
2.4.3 Hazard Risk Management .....	22
2.4.4 Communication And Consultation (Workers & Community).....	23
2.4.5 Emergency Management Plan .....	23
2.4.6 Emergency Control Centre .....	23
2.4.7 Reference To Ifc Environmental Health And Safety Guidelines.....	24
2.5 Biodiversity Conservation Management Plan (ESS6).....	24
2.5.1 Applicability Of Bio Conservation And Management Plan (BCMP) To A Sub-Project.....	24
2.5.2 Sub Project Description.....	24
2.5.3 Inventory Of Terrestrial And Aquatic Flora Fauna.....	24
2.5.4 Likely Impact Of Project Activities On Biodiversity Areas. ....	24



2.5.5 Conservation And Management Plan .....	24
2.5.6 Monitoring, Compliance Reporting And Budget .....	25
2.6 Tribal Development Plan (ESS7) .....	25
2.6.1 Applicability Of Tribal Development Plan (TDP) To A Sub-Project .....	25
2.6.2 Tribal Groups In The Area .....	26
2.6.3 Previous Consultations .....	26
2.6.4 Social Impacts, If Any .....	26
2.6.5 Measures To Avoid, Minimize Impacts, If Any .....	26
2.6.6 FPIC .....	26
2.6.7 Action Plan To Be Implemented With EAP .....	27
2.7 Cultural Heritage Protection Plan (ESS8) .....	27
2.7.1 Scope Of Cultural Heritage Protection Plan (CHPP):.....	27
2.7.2 Chpp Preparation And Approval .....	28
2.7.3 Contents Of Site Specific CHPP.....	28
2.8 Stakeholder Engagement Plan (ESS10).....	28
2.8.1 Identification Of Stakeholders .....	28
2.8.2 Stakeholder Engagement And Project Cycle .....	29
2.8.3 Timelines For Information Disclosure And Feedback .....	31
2.8.4 Monitoring And Reporting .....	31
<b>Chapter 3: Environmental And Social Mitigation And Monitoring Plan.....</b>	<b>32</b>
3.1 Purpose Of ES Mitigation Management And Monitoring.....	32
3.2 Esmitigation and Monitoring Plan - Action Responsibility Matrix.....	41
<b>Chapter 4. Implementation Arrangements And ESMP Budget.....</b>	<b>43</b>
4.1 Implementation And Supervision Arrangements.....	43

#### List of Annexure

Annexure 1: Outline Of Contractor's ESMP .....	47
Annexure 2: Sub-Project Specific E&S Sensitive Information.....	50
Annexure 3: Sample Code Of Conduct (Coc) .....	52
Annexure 4: Grievance Redressal Mechanism (Sample .....	56
Annexure 5: Internal Complaint's Committee (Sample .....	57
Annexure 6: Standard Operating Procedure (Sop).....	59
Annexure 7: Safety Signs .....	60
Annexure 8: Accident Reporting .....	62
Annexure 9: Covid Protocol .....	63
Annexure 10: Traffic Management Plan .....	65
Annexure 11: Sop For Labour Camp .....	67
Annexure 12: Emergency Preparedness Plan .....	69
Annexure 13: Fire Fighting Appliances Types Of Extinguishers Suited For The Three classes of fire is As follows.....	70



## ACRONYMS

CPCB:	Central Pollution Control Board
CPMU:	Central Project Management Unit
CWC:	Central Water Commission
DRIP:	Dam Rehabilitation and Improvement Project
EAP:	Emergency Action Plan
EMC:	Engineering and Management Consultant
ESCP:	Environment and Social Commitment Plan
ESDD:	Environmental and Social Due Diligence
ESF:	Environmental and Social Framework
ESHS:	Environmental, Social, Health and Safety
ESIA:	Environmental and Social Impact Assessment
ESMF:	Environmental and Social Management Framework
ESMP:	Environmental and Social Management Plan
ESS:	Environmental and Social Standard
GBV:	Gender Based Violence
GRM:	Grievance Redressal Mechanism
HIV:	Human immunodeficiency virus
IA:	Implementation Agency
LMP:	Labour Management Procedure
LPG:	Liquefied Petroleum Gas
MMP:	Muck/Debris Management Plan
MPR:	Monthly Progress Report
NDMA:	National Disaster Management Authority
NGO:	Non-Governmental Organization
OHS:	Occupational Health & Safety
OHSMP:	Occupational Health and Safety Management Plan
OHSP:	Occupational Health and Safety Plan
PPE:	Personal Protective Equipment
PUC:	Pollution Under Control
QPR:	Quarterly Progress Report
RCP:	Resource Conservation Plan
SDMA:	State Disaster Management Authority
SEF:	Stakeholder Engagement Framework
SEP:	Stakeholder Engagement Plan
SPMU:	State Project Management Unit
ST:	Schedule Tribe
TDP:	Tribal Development Plan
TPA:	Third Party Agency
WB:	World Bank



**BLANK PAGE**



## CHAPTER 1: PROJECT OVERVIEW AND FINDINGS OF ESDD

### 1.1. PROJECT OVERVIEW

The Dam Rehabilitation and Improvement Project Phase II and Phase III (DRIP Phase II & Phase III) initiated by Ministry of Jal Shakti through Central Water Commission, with an objective to cover more States and more dams (after DRIP Phase I) across India to improve the safety and operational performance of these selected dams. This new Scheme will further strengthen the efforts of Government of India beyond ongoing DRIP Phase I. The project would continue to finance structural improvements along with dam safety institutional strengthening which shall break with the prevailing build-neglect-rebuild approach by giving greater emphasis to establishing innovative financing mechanism for regular O&M and dam rehabilitation, enhancing State capabilities to manage these critical assets through institutional strengthening, and introducing risk-informed dam safety management. The project development objective (PDO) is to increase the safety of selected dams and to strengthen institutional capacity for dam safety in participating States. The project components are as follows:

**Component 1:** Rehabilitation and Improvement of Dams and Associated Appurtenances, focusing on structural and non-structural measures at selected project dams. The proposed interventions will include, but not be limited to, around 35-40 kind of rehabilitation activities as done in ongoing DRIP. In addition, all important non-structural activities will also be taken up. In addition to these interventions, the project will require each rehabilitated dam to have basic instrumentation and could also support the development of additional systems to detect and respond to risks promptly, such as flood forecasting systems, early warning systems, data management and analysis software, and standardized dam safety instrumentation (i.e., Supervisory Control and Data Acquisition [SCADA]).

**Component 2:** Dam Safety Institutional Strengthening, focusing on regulatory and technical frameworks for dam safety assurance. The activities to be carried out will include, but not be limited to, targeted training nationally and internationally to all partner agencies, development of Management Information Systems (MIS) and other programs to capture and analyze data for long-term planning and guiding of dam operations; support to the further development within CWC of the Dam Health and Rehabilitation Monitoring Application (DHARMA) program, support to the revision of existing guidelines on dam safety and preparation of new guidelines, as needed; rapid risk screening of dams, stakeholders consultation meetings for dissemination of prepared emergency action plans, updation of seismic hazard mapping of country, capacity building of academic and central institutions, public outreach programs, construction supervision & quality assurance activities etc.



**Component 3:** Incidental Revenue Generation for sustainable operation and maintenance of dams; in order to ensure long term sustainability of operations & maintenance of existing dams, it is proposed to encourage the dam owners to explore the incidental revenue generation through innovative ideas i.e. Development of tourism, fisheries, secondary sources of power generation (hydel as well as solar), water recreation activities etc. and divert some part of this generated revenue for O&M of a given dam. Few pilot dams can be selected to experiment this innovation.

**Component 4:** Project Management; the overall responsibility for project oversight and coordination will rest with the CDSO of CWC. This Organisation will act as the Central Project Management Unit (CPMU). The CPMU will be assisted by a management and engineering consulting firm. Each state and other agency will establish a Project Management Unit (SPMU) attached to the Chief Engineer's (CE) office in charge of the SDSO or any such similar arrangement in power utilities. This Unit will have direct responsibility for the coordination and management of the project at state level.

The primary beneficiaries of the project are the communities that live in dam breach flood inundation areas and the communities that depend on water, irrigation and electricity services provided by the dams that could be compromised by poor dam performance or failure. The Project will be taken up in 19 states covering 300 dams.

## 1.2. OBJECTIVE AND CONTEXT OF ESMP

A project level ESMF has been prepared and disclosed. In compliance with the ESMF, Environmental and Social Due Diligence has been carried out employing E&S risk screening templates. ESMF mandates that for all Low and Moderate Risk projects, a standard ESMP shall be prepared, which will be updated based on the sub project specific activities. Accordingly, this Standard ESMP is prepared describing the process to manage the impacts identified during the ESDD. The ESMP also determines the implementation schedule, roles and responsibilities, reporting and monitoring requirements. The management plans included in this ESMP outline the environmental and social mitigation measures and management controls to be implemented in compliance with the E&S commitments.

This ESMP is a live document and is subjected to periodic review and updates. The Implementation Agency and contractors are primarily responsible for the implementation of the ESMP. Environmental and social management plans covering various phases, prepared as part of this ESMP shall be updated in line with the dynamics of project progress and stakeholder engagement inputs. If during the operationalization of this ESMP, new conditions emerge and risks and impacts differ from that identified in the ESDD, a new ESMP may be prepared adapting to the new conditions.



### 1.3. SUB PROJECT DESCRIPTION– KODAYAR DAM I

- 1.3.1.** The Kodayar Dam I across River Kodayar in Kanyakumari district during the year 1963 to 1972. This is a masonry gravity dam. The dam is located in Kanyakumari District at Upper Kodayar, TamilNadu State. The nearest Town is Kallidaikurchi, which is 47 Km and Tirunelveli, which is 35 Km away from the Dam. Nearest airport is Tuticorin, which is 156 Km away from Dam and nearest Railway station is Kallidaikurchi, which is 47 Km. This dam is a masonry gravity dam with a height of 87.78 m and a length of 166m. It is a storage cum Forebay for Kodayar Power House (1x 60 MW ) located at lower Kodayar. Apart from the water received from its own catchment, the water collected at Chinnakuttiyar Dam (from its catchment) as well as water diverted from Kuttiyar dam also, pumped into Kodayar dam-I reservoir to augment its storage. After generation of 60MW in Kodayar Power House I, the tail water is let into Kodayar Dam-II located downstream for generating power at Kodayar Power House II (1x40 MW). Ultimately, all the water reaches into Pechiparai reservoir of TNWRD for irrigation.

Salient features of the project area are reported below:

	<b>Project</b>	<b>Kodayar Dam-I</b>
1.	Location	Upper Kodayar, Kanyakumari District
2.	River	Kodayar
3.	Purpose	Hydro Power Generation
4.	Construction Period	1963 – 1972
5.	Latitude	8° 31' 19" N
6.	Longitude	77° 21' 35" E
	<b>Reservoir</b>	
7.	Catchment area	29.12 Sq.km
8.	Water spread Area	8.30 Sq.km
9.	Gross capacity	98.69 M.Cum
10.	MWL	+1325.90 m
11.	FRL	+1325.90 m
	<b>DAM</b>	
12.	Type	Masonry – Gravity
13.	Top of Dam	+1328.32 m
14.	Lowest river bed level	+1259.74 m
15.	Deepest foundation level	+1240.54 m
16.	Highest from deepest foundation	87.78 m
17.	Length	166 m
	<b>SPILLWAY</b>	
18.	Discharge capacity	257 Cumecs
19.	Crest length	9.14 m
20.	Crest level	+1319.80 m
21.	Type of gate	Lift Type
22.	Size & No. of gate	9.14 x 6.1 m; 1 No.
	<b>SCOUR VENT</b>	
23.	Size	1.52 x 2.13 m
24.	Sill level	+1290.56 m
25.	Regular gate	3.00 x 2.31 m
26.	Emergency gate	3.00 x 3.23 m
	<b>INTAKE</b>	



27.	Discharge capacity	8.21 Cumecs
28.	Size	2.135 m dia.
29.	Sill level	+1290.56 m
	<b>TUNNEL</b>	
30.	Length	3147.97 m
31.	Size	2.13 x 2.13 m
32.	Shape	Horse shoe
33.	Discharge capacity	8.21 Cumecs



**View of Downstream face of the Dam**



**View of Kodayar Dam I Reservoir**







#### **1.4. PROPOSED INTERVENTIONS/ ACTIVITIES AND INTENDED OUTCOMES**

Dam Safety Review Panel (DSRP) constituted by CWC, Government of India has inspected and made a review of Kodayar dam I on 08/12/2020 and recommended measures to improve the safety and performance of dam and associated appurtenances in a sustainable manner, and also to strengthen the dam safety institutional set-up.




The objectives of the project are to be achieved through investments for physical and technological improvement activities, managerial upgrading of dam operations, management and maintenance, with accompanying institutional reforms. The project will improve the safety and operational performance of dam and mitigate risks to ensure safety of downstream population and property. The following rehabilitation proposals as described in the PST have been formulated based on DSRP recommendations and these proposals form the basis for preparation of present ESDD report

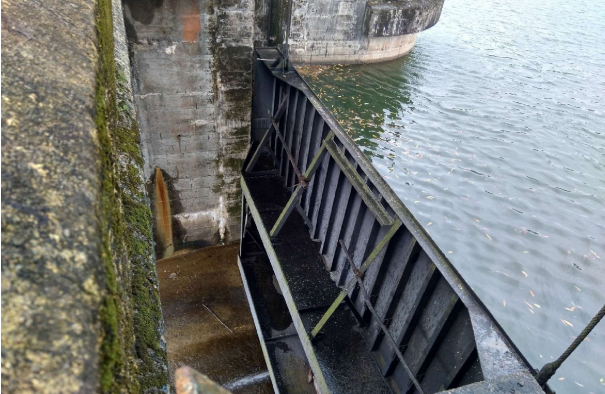

**Figures 1.1 and 1.2** provide photographs of key infrastructure proposed for rehabilitation works and also major interventions locations.

	
<p>Water jetting inside the Scurvent gate</p>	<p>View of Saddle dam-I of right flank</p>
	
<p>Downstream face of Saddle dam II (R/F)</p>	<p>View of Approach road to Saddle dams I &amp; II</p>
	
<p>Leakage notice spillway gate bottom</p>	<p>Seepage from drainage saddle dam II (R/F)</p>



	
<p>Leaching on the Downstream face of dam (L/F)</p>	<p>Leaching on the Downstream face of dam (R/F)</p>
	
<p>Downstream face with Algae growth</p>	<p>View of Vertical shafts Saddle dam-I of right flank</p>



**Figure 1.1: Selected Photographs of Improvement/Intervention area**



**Figure 1.2: Project Area showing major intervention locations of Kodayar Dam I**

### 1.5 ESDD FINDINGS AND KEY IMPACTS TO BE ADDRESSED

ESDD has been carried out considering the above proposals/interventions. The screening and site assessment exercise has identified the nature of risk and impacts, with level of risk and the outcomes are documented in ESDD report. The risks/impacts identified are related to labour employment and working conditions, pollution generation from rehabilitation work and impact on physical environment, SEA/SEAH and GBV risks. These risks are low to moderate and localised, short term and temporary in nature which can be managed following management plans and guidelines.

Environment risks of air, water, noise; land use, soil and resource use for most of the activities are moderate as well as social risks of labour. Environment risks of pollution downstream and upstream is categorised as Moderate for some of the activities along with that of labour camp. As per ESMF, OHS is considered a substantial risk activity for all sub-projects and is being treated separately through OHS plan in accordance with WBG Environmental Health and Safety (ESHS) Guidelines and shall be applicable to all sub-projects. Hence it was not being considered under screening criteria. Occupational health and safety is considered an important requirement and shall be managed as per above stated OHS plan and will be part of Contractor's ESMP.

Based on ESDD findings, WB Environmental & Social Standards (ESS) applicability analysis and recommended management plan is given at Table 1.1.



Table 1.1 WB-ESS Applicability Analysis and Recommended management plan

<b>WB-ESS</b>	<b>Recommended Management Plan</b>	<b>Applicability To Kodayar Dam I</b>
ESS1: Assessment and Management of Environmental and Social Risks and Impacts	Gender Based Violence or SEA/SH related actions	Applicable
ESS2: Labour and Working Conditions	Labour Management Procedure including Occupational health and Safety	Applicable
ESS3: Resource Efficiency, Pollution Prevention and Management	Pollution Prevention and Environment Quality Management Plan including Muck/Debris Management	Applicable
ESS 4: Community Health and Safety	Community Health and Safety Plan	Applicable
ESS 5: Land Acquisition, Restrictions on Land Use and Involuntary Resettlement	Resettlement Action Plan/ Livelihood improvement Plan	Not Applicable
ESS 6: Biodiversity Conservation and Sustainable Management of Living Natural resources	Biodiversity Conservation Plan	Not Applicable
ESS 7: Indigenous Peoples/Sub-Saharan African Historically Underserved Traditional Local Communities	Tribal Development Plan	Not Applicable
ESS 8: Cultural Heritage	Cultural Heritage Protection Plan	Not Applicable
ESS 10: Stakeholder Engagement Plan	Stakeholder Engagement Plan	Applicable

The above recommended plans are discussed in detail in Chapter 2.



## CHAPTER 2: ENVIRONMENTAL AND SOCIAL MANAGEMENT PLANS

The E&S management plans prepared for the risks and impacts identified as part of ESDD are presented hereunder. Each plan includes mitigation measures specific to the risks and impacts and where applicable, sets out the framework for other plans and procedures to be developed later in the Project. Constructors contractors will develop and implement their own site specific C-ESMPs GENDER BASED VIOLENCE OR SEA/SH RELATED ACTIONS (ESS1).

2.1 The following key actions are to be ensured during implementation:

S. No.	Key Action to address GBV/SEA/SH Risks	By Whom
1	Clearly define SEA/SH requirements in Bid-documents and also the requirement for a CoC which addresses SEA/SH, using Standard WB procurement documents	SPMU
2	Operationalize or constitute Internal Complaints Committee as per Prevention of Sexual Harassment at Workplace procedure	SPMU
3	Implement appropriate project-level activities such as: separate, safe and easily accessible facilities for women and men in the place of work and the labour camps. (e.g. toilets should be located in separate areas, well-lit) display signs that the project site is an area where SEA/SH is prohibited.	Contractor (implementation) GBV Focal Point at SPMU. Engineerin Charge
4	Ensure Codes of Conduct are clearly understood and signed by those with a physical presence at the project site; Train project staff on the behaviour obligations under the CoCs and Disseminate CoCs (including visual illustrations) and discuss with employees and local communities.	Engineer in Charge Contractor
5	Undertake regular M&E of progress on SEA/SH prevention and response activities, including reassessment of risks as appropriate.	GBV Focal Point at SPMU/IA

Implementation costs would include: preparation of sign boards, posters, conducting of awareness trainings by Implementing Agency and also by Contractor.



## 2.2 LABOR MANAGEMENT PROCEDURE (ESS2)

### 2.2.1 OVERVIEW OF LABOUR USE IN THE PROJECT

**Number of Project Workers:** Approximately 50 workers at different points of time (Direct workers, Contracted workers and Community workers) shall be engaged for the rehabilitation works

**Characteristics of Project Workers:** As per the proposed execution strategies for all Low to Moderate risk sub-projects, the following categories of project workers are identified:

- i) Direct workers – all the existing dam site officials including those sent on deputation from other departments involved in the project activities;
- ii) Contracted workers - all IAs would engage Contractors to undertake rehabilitation works; agencies/firms to support core service functions such as SCADA systems, etc. These contractors shall bring skilled Migrant workers for some of more specialized tasks; and
- iii) Community workers (or volunteers particularly for EAP).

**Timing of Labor requirements:** See Table below:

S.No.	Type	Numbers	Locations	Duration	Skills required
1	Direct Workers (Project officials)	3-5	Dam site	Throughout	Executive and Supervisory
2	Contracted Workers	30-50	Dam site	18 months	Varied (skilled, semi skilled)
3	Community Workers	10-15	Villages/areas in the vicinity of the dam	Only during EAP implementation	Community facilitation skills

### 2.2.2 ASSESSMENT OF KEY POTENTIAL RISKS

Labour related risks would include:

- Safety issues while at work like injuries/accidents/ fatalities Occupational health and safety risks due to exposure of workers to unsafe conditions while working at heights, working using lifts, handling of equipment and machinery, exposure to air and noise pollution etc. will be addressed through OHS guidelines.
- Short terms effects due to exposure to dust and noise levels, while at work
- Inadequate accommodation facilities for labour, including inadequate sanitation and health facilities
- Discrimination in Employment (e.g. abrupt termination of the employment, working conditions, wages or benefits etc.)
- Sexual harassment at work
- Absence or inadequate or inaccessible emergency response system for rescue of labour/workforce in situations of natural calamities.
- Health risks of labour relating to HIV/AIDS and other sexually transmitted diseases
- Non-payment of wages
- Unclear terms and conditions of employment



- Discrimination and denial of equal opportunity in hiring and promotions/incentives/training opportunities
- Denial for workers' rights to form worker's organizations, etc.
- Absence of a grievance mechanism for labour to seek redressal of their grievances/issues

## **Brief overview of labor legislation: Occupational health and safety: Refer to Annexure 1**

### **2.2.3 RESPONSIBLE STAFF**

See Table below for list of key activities with responsibilities:

<b>S.No.</b>	<b>Activity</b>	<b>Responsibility</b>
1	Engagement and management of Contractors	SPMU of IA (TANGEDCO)
2	Engagement and management of Sub-Contractors	Contractor
3	Occupational Health and Safety (OHS)	E&S Specialist, Dam Manager and Engineer-In-Charge
4	Training of Workers	E&S Specialist, Dam Manager and Engineer-In-Charge
5	Addressing worker grievances	Contractor (with oversight by IA)

### **2.2.4 POLICIES AND PROCEDURES**

These are listed below under the following sub-headings: i) Incidents and Accident Notification; ii) GBV/SEAH related iii) Occupational Health and Safety; and iv) COVID considerations.

- i) **Incidents and Accident Notifications:** The contractor will promptly notify to the IA/SPMU within 24 hours any major incident or accident having significant impact on the environment, tangible cultural heritage, communities, the public or workers. They will provide sufficient detail regarding the incident or accident, indicating immediate measures taken to address it, and including information provided by any contractor and supervising entity. Further the SPMU will appraise this to CPMU and WB.
- ii) **GBV/SEAH related:** More than 95% of the contract labour is expected to be men, and women's participation as contract labour or community labour is going to be very low. Contractors will need to maintain harmonious relations with local communities by ensuring laborers/workers adhere to Code of conduct (CoC). The CoC commits all persons engaged by the contractor, including sub-contractors and suppliers, to acceptable standards of behavior. The CoC will include sanctions for non-compliance, including non-compliance with specific policies related to gender-based violence, sexual exploitation and sexual harassment (e.g., termination). The CoC will be written in plain language and signed by each worker to indicate that they have:
  - received a copy of the CoC as part of their contract;
  - had the CoC explained to them as part of induction process;
  - acknowledged that adherence to this CoC is a mandatory condition of employment;
  - understood that violations of the CoC can result in serious consequences, up to and including dismissal, or referral to legal authorities.



To mitigate potential risks related to on-site safety and GBV, the Contractor/ will undertake actions as given in Table below:

S.No.	Action	Timelines
1	Separate, safe and easily accessible facilities for women and men in the place of work and the labour camps. (e.g. toilets should be located in separate areas, well-lit)	Throughout construction period
2	Display signs that the project site is an area where SEA/SH is prohibited.	Throughout construction period
3	Ensure Codes of Conduct are clearly understood and signed by those with a physical presence at the project site;	Upon joining
4	Train project staff on the behavior obligations under the CoCs and Disseminate CoCs (including visual illustrations) and discuss with employees and local communities.	Periodic; every six months

### iii) Occupational Health and Safety

IA is committed to:

- Complying with legislation and other applicable requirements which relate to the occupational health and safety hazards.
- Enabling active participation in OH&S risks elimination through promotion of appropriate skills, knowledge and attitudes towards hazards.
- Continually improving the OH&S management system and performance.
- Communicating this policy statement to all persons working under the control of IA with emphasis on individual OH&S responsibilities.
- Availing this policy statement to all interested parties

To avoid work related accidents and injuries, the contractor will:

- Provide adequate number of good quality appropriate PPEs – helmets, gum boots, safety belts, safety harness, gloves, overalls, ear plugs, face masks, life jackets etc.
- provide Training to workers on use of appropriate PPEs and how to respond during emergency
- Display EHS instructions at site
- Make provision of First aid boxes with availability and trained first aiders at site
- Ensure availability of portable fire extinguishers
- Ensure safe handling of welding gas LPG, oxygen or acetylene cylinders.
- Inform of assembly area in the emergency scenario
- Provide adequate number of toilets and arrangement for potable drinking water for all workers.
- Ensure proper disposal of solid waste at designated permitted sites/landfill allocated by the local authorities;

Further to enforce the compliance of environmental management, contractors will be responsible and liable for safety of site equipment, labours and daily workers attending to the construction site and safety of citizens for each work site, as mandatory measures.



### **Occupational Health and Safety Monitoring**

OHS compliance monitoring will be carried out by designated E&S Expert every month. Contractor will provide compliance in initial report to Engineer in charge and thereafter submit a compliance report every 3 months. Following shall be covered as part of OHS monitoring:

- Health check-up records of workers
- Accident hot spots on transport route, if any
- Training and awareness of labour – OHS, Emergency Management, Use of PPEs
- Identification of hazardous working locations and marking
- Emergency response procedure
- Availability of PPEs – types, numbers
- Accident reporting

### **Communication and Consultation (Workers)**

Workers consultation will be regular features. However this aspect shall be as per consultation process defined under other plans and ESS4.

### **Training and Records**

Contractor will provide training to all workers before start of work and thereafter every three months. He will maintain training records and share the details with E&S experts of the dam as part of his quarterly progress report. The training should cover the following:

- General awareness about the site, type of works to be carried out and risks involved
- Use of appropriate PPEs for different types of works including dust masks and ear muffs
- Following work instructions for hazardous/risky operations as marked on site
- How to act during emergency including basic rescue operations and accident reporting
- Location of first aid boxes and fire extinguishers and how to use them



### **Emergency Preparedness and Management**

Emergency Preparedness and Management Plan shall be followed as given under ESS 4

### **Reference to World Bank Group –(WBG) Environmental Health and Safety (EHS) and Other Guidelines**

The WBG Guidelines of Environmental Health and Safety (WBGEHS) provide detailed guidance note on health and safety requirement and good practices. The WBGEHS guidelines are intended to be used in conjunction with Indian legislation on OHS at construction sites and shall be referred by contractor and IAs while finalizing site specific contractor's EHS management plan.

iv) COVID Considerations: Refer Annexure 9.

#### **2.2.5 AGE OF EMPLOYMENT**

The minimum age of employment for this project shall be 18 years and to ensure compliance, all employees will be required to produce a valid proof of age. If any contractor employs a person under the age of 18 years, that contractor will not only be terminated by IA but also be reported to the authorities.

#### **2.2.6 TERMS AND CONDITIONS**

Terms and conditions for three types of workers are presented below:

- i. The Direct Workers (Dam officials, government officials) are governed by their employment agreements with the Water Resources Department
- ii. Contractors will also be required to comply with the most current Regulation of Wages for the Building and Construction Industry which is issued by the Government and reviewed on a regular basis. The Minimum Wage Act specifies the minimum wages, hours of work, overtime pay, leave entitlements, travelling and Subsistence Allowances and the issue of protective clothing. Before a contract is awarded, contractor is required to certify in writing that the wages, hour and conditions of work or persons to be employed by him on the contract are not less favourable than those contained in the most current wages regulation issued by the Labour Commissioner. Where a contractor fails to comply with this requirement, the contract with the contractor may be withdrawn as an approved contractor upon recommendations of the Labour Commissioner.

In ensuring full compliance with the law in this regard, contractors will be required to furnish with copies of the labour license and/ or copies of contract of all its workforce. As a monitoring mechanism, a contractor shall not be entitled to any payment unless he has confirmed that all employment conditions of the contract are being complied with. The IA would intervene if the contractor defaults in the payment of wages due to any of its employees.

'Community Workers' is further detailed in following sections.



### **2.2.7 GRIEVANCE MECHANISM**

The Grievance Mechanism for Workers will be organized as follows.

- i. **Direct Workers (Project Officials):** The Executive Engineer, Dam Authority, will be responsible for providing guidance and advice on all worker related grievances and their redressal, in line with the state and national legislation and the LMP.
- ii. **Contract Workers:** While the Contractor will have his own GRM, the IA (Water Resources Department will have oversight) and the overall responsibility for ensuring the establishment and implementing the GRM for project workers. In this regard, the Executive Engineer will be responsible to ensure that the Contractor has established and operationalized the contract workers grievance redress mechanism. In this, Contractor will be supported by Environment and Social nodal officers by IA designated for the purpose. S/he will also be responsible for tracking and resolving workers grievances. S/he shall maintain records where grievances and complaints, including minutes of discussions, recommendations and resolutions made, will be recorded.
- iii. **Community Workers:** The Executive Engineer, Dam Authority, will be responsible for providing guidance and advice on all community worker related grievances with this LMP.

The designated Social Expert in SPMU will provide overall implementation and capacity building support on resolving all workers grievances and will support the Executive Engineer in this regard. S/HE will also include workers grievance status in the progress report. Grievances will continue to be received through established communication channels. Workers will also be able to submit their grievances through the district Labour Department, whose contacts will be shared with all the contractors and worksites.

### **2.2.8 CONTRACTOR MANAGEMENT**

IA will ensure that contractor monitor, keep records and report on terms and conditions related to labour management. The contractor must maintain records with evidence of all payments made, including social security benefits, pension contributions or other entitlements, as applicable based on workers engagement i.e.-fixed term contract, full-time, part-time or temporary. The application of this requirement will be proportionate to the activities and to the size of the contract, in a manner acceptable to CPMU and the World Bank:

Labour conditions: records of workers engaged under the Project, including contracts, registry of induction of workers including CoC, hours worked, remuneration and deductions (including overtime), collective bargaining agreements;

Safety: reportable incidents and corresponding Root Cause Analysis (lost time incidents, medical treatment cases), first aid cases, high potential near misses, and remedial and preventive activities required (for example, revised job safety analysis, new or different equipment, skills training, and so forth).



Workers: number of workers, indication of origin (local and migrant), gender, age with evidence that no child labour is involved, and skill level (unskilled, skilled, supervisory, professional, management).

Training/induction: dates, number of trainees, and topics.

Details of any security risks: details of risks the contractor may be exposed to while performing its work; the threats may come from third parties external to the project. Worker grievances: details including occurrence date, grievance, and date submitted; actions taken and dates; resolution (if any) and date; and follow-up yet to be taken; grievances listed should include those received since the preceding report and those that were unresolved at the time of that report.

## **2.3 RESOURCE EFFICIENCY AND POLLUTION PREVENTION (ESS3)**

### **2.3.1 POLLUTION PREVENTION AND ENVIRONMENT QUALITY MANAGEMENT PLAN (PPEQMP)**

Dam rehabilitation work in general can be categorised as civil work including paint work and hydro-mechanical work. requiring labour involvement for works, use of resources such as raw material, water and power during construction, pollution generation from storage and handling of material, generation of waste, use of paints and other chemicals for construction activities and generation of hazardous waste, transportation of raw material, etc. As all the proposed structural interventions are within the dams' premises, no adverse impacts are envisaged on communities including on the disadvantaged or vulnerable people.

Resource Efficiency, Pollution Prevention and Management plan is prepared to address potential risks identified with respect to resource use and pollution generation from civil, hydro-mechanical and painting work and also from labour camps and colonies.

### **2.3.2 OVERVIEW OF PPEQMP**

#### **a) Water Management**

The proposed intervention activities are not expected to impact water resources as the proposed interventions are neither crossing, altering or disturbing drainages nor impacting ground water resource in any form. Use of resources such as water and power will be optimized before start of work.

Construction related impacts and risks for water quality include:

- Accidental release of fuel or chemicals and contamination from poor waste management practices can affect surface and groundwater; although quantum of waste is expected to be small.
- Fuel/oil leakage from construction machinery working near water bodies
- Construction work along river bank
- Generation of sanitary wastes from labour colony and construction sites finding way to water bodies

Pollution prevention and control measures to avoid surface water pollution shall include:



- Labor camp will have adequate sanitation arrangement in terms of mobile/fixed toilet with arrangement of sewage collection and disposal. No wastewater from the camp/work force site shall be discharged directly without any treatment in to any surface water channels or drain, which eventually joins surface waterbodies.
- The oil/lube storage shall be under roofed areas with impermeable cement concrete surfaces and provided with separate drainage system with oil separators. No discharge from oil/lube storage areas shall be directly discharged in to any open surface water channel/ streams.
- No construction debris and/or spills of construction materials are dumped on to stream waterway.
- Construction work along river bank shall be done in lean season when surface water level has receded and clear construction area is available.
- Activities like Rip-rap replacement and work on upstream side of dam (reservoir side) will be taken up only when the water level is low and clear work area is available. Adequate protection needs to be provided to avoid spillage of chemicals/construction material in reservoir.

**b) Air Quality Management**

Construction activities can give rise to dust emissions if not effectively managed and have the potential to affect receptors near to the main construction sites due to dust generated from demolition, excavation, operation of construction equipment and machinery, increased movement of vehicles, onto the local road network. Earth works will result in exposed areas of soil which will potentially generate dust when the weather is windy. The level and distribution of dust emissions varies according to the duration and location of activity, weather conditions, and the effectiveness of suppression measures.

Gaseous emission during construction will be from machinery, equipment and vehicles used for material transportation. The operation of vehicles and equipment will result in emissions of carbon monoxide, sulphur dioxide, and oxides of nitrogen. In particular, all commercial vehicle driven with diesel fuel is often used in India. Impact is expected to be localised. Keeping in view the quantum of work and requirement of raw material, there will be only 4-5 vehicles required and therefore emission on village road due to vehicular movement will not be significant.

As the project is presently operational and the interventions are not going to alter the project operation in any manner, no operational phase impacts are envisaged on ambient air quality.

Pollution prevention and control measures to avoid air pollution shall include:

Among the air pollutants, dust levels in term of  $PM_{2.5}$  and  $PM_{10}$ , is the most significant. In order to prevent and control the dust levels, the following measures are to be strictly adhered to:



- The contractor/transporter shall carry valid PUC (Pollution Under Control) certificate and only compliant vehicles shall be deployed during construction.
- The vehicles and equipment used during construction should be well maintained, to ensure minimum emissions. Engineer in Charge will carry out physical inspection to ensure compliance.
- The contractor shall provide wind barrier, if required, depending on most prevailing wind direction and presence of sensitive receptors at downwind side, at perimeter of construction site to arrest or blowing of suspended particle.
- Regular sprinkling of the water will be done on construction sites for dust suppression if there is potential of dust emission from storage or handling of loose material.
- If power connection is not available, Mobile DG sets may be used for lighting only during construction phase and they should meet emission and noise standards as per guidelines/standards issued by CPCB.
- All the construction workers and other staff, who get directly exposed to dust, should necessarily be provided with dust masks.

**c) Noise and Vibration Control**

Sources of noise will be the vehicles and equipment for construction at the project sites. Due to construction activity in the area, noise levels will increase during the period of construction, however, they will remain limited to the work area mainly where construction activity will progress.

Impact of noise generation due to operation of construction machines and equipment is the exposure of workers operating these machines and other who are working in the surrounding. Such impacts can become significant if they are exposed to high noise for long hours continuously.

Pollution prevention and control measures to avoid Noise pollution shall include:

- DG sets, if required, will have a valid Type Approval Certificate and Conformity of Production certificate as per CPCB guidelines.
- All the construction equipment will be required to use available noise suppression devices and properly maintained mufflers.
- Workers in high noise area, will be provided with ear muffs. Workers exposure (time duration) to high noise will also be controlled.
- Minimize the use of noise producing equipment during night hours to avoid the disturbance to locals and wild animals of surrounding area.
- Vehicles to be equipped with mufflers recommended by the vehicle manufacturer.
- Movement of vehicles on village roads especially heavy vehicles for transportation of construction material, equipment, etc. shall be done during day time only.



**d) Waste Management from Hydro-mechanical works**

Project interventions include hydro-mechanical work such as repair/replacement of hoists and ropes, repair and general maintenance and upkeeping of gates, etc. These activities will generate waste in terms of replaced parts, packaging material, empty containers, use and disposal of oil & grease, iron scrap, etc. There will be a mix of hazardous and non-hazardous wastes. It is important to have a plan ready for disposal of such wastes before start of the activity.

Pollution prevention and control measures with respect to waste management shall include:

Project engineer needs to identify all the waste generated from hydro-mechanical work include replaced parts with estimated quantities and categorisation as hazardous and non-hazardous waste. Storage and disposal of removed parts need to be planned by Executive Engineer; separately for hazardous waste which will be given to authorised vendors only.

**e) Muck/Debris Management**

Rehabilitation work will generate muck and construction debris due to repair and demolition works such as removal and fresh laying of rip-raps, removal of top layer during road repairs, operation of construction equipment and machinery and waste generation thereof, etc.

Pollution prevention and control measures in respect of Muck/Debris management shall include:

- Muck/debris disposal site shall be identified by contractor and concerned Executive Engineer together and necessarily avoid natural water courses.
- While identifying such locations, endeavor would be to find low lying areas nearby so as to avoid effort of transporting muck/debris.
- Area on the course of natural drainage should be avoided.
- The construction debris from all operational areas shall be regularly scavenged and disposed off at identified disposal sites only.
  - No dump site shall be located in forest area.
  - No dump site shall be located on agricultural area.
  - The Contractor shall educate his workforce on issues related to disposal of waste.
  - The debris disposal sites have to be suitably rehabilitated by levelling and restoring to original conditions
  - If required, grass and local shrubs should be planted to rehabilitate the site.

**2.3.3 HOW WATER AND OTHER RESOURCE USE WILL BE PLANNED**

Resource planning will be done by contractor in consultation with engineer in charge. After award, the contractor will make an estimate of the raw material requirement, sources for procurement and transportation route. Contractor will discuss the plan with Engineer in Charge at site and get approval.



Material to be procured from quarry/borrow area, shall be identified by contractor along with source. Approval status will be submitted to engineer in charge for consent.

Requirement of water and power at various locations for construction work and labour camp shall be established by contractor and discussed with Engineer in charge. Locations, where DG power is to be used, shall be identified along with location of DG set and its noise and emission impacts on labour and community. Mitigation measures such as ear muffs for labour and sound barrier for community, if required shall be established.

#### **2.3.4 ENVIRONMENTAL QUALITY MONITORING PLAN AND PROTOCOLS**

This being rehabilitation work limited to dam area only with localised impacts which can be managed by implementing standard ESMP, environment quality monitoring is not required. However, keeping in view that some of the dams are located in proximity to protected areas, environmental quality monitoring will be carried out at such dams only.

Environment Quality monitoring requirements for dam located in proximity to protected areas are tabulated below:

<b>Activity</b>	<b>Parameters</b>	<b>Locations</b>	<b>Frequency</b>	<b>Responsibility</b>
Ambient Air Quality	PM <sub>2.5</sub> , PM <sub>10</sub> and SO <sub>2</sub> for 24 hours	At two major location of rehabilitation works to be identified by E&S Expert	Once before start of construction, once during the construction period and one at end of rehabilitation work	Contractor through NABL accredited Lab
Sound Levels	dB(A) levels – day and night equivalents – hourly reading during day and night time for 24 hrs	At two major location of rehabilitation works to be identified by E&S Expert	Once before start of construction, once during the construction period and one at end of rehabilitation	Contractor through NABL accredited Lab
Wastewater discharge	Physical inspection to ensure wastewater from rehabilitation work is not being disposed off in river	All rehabilitation worksites using water	Once every month	Engineer in charge through E&S Expert
Muck and debris handling and disposal	Physical inspection to ensure muck/debris from rehabilitation work is being securely disposed off at identified and approved location	All rehabilitation worksites generating muck/debris	Once every month	Engineer in charge through E&S Expert



Storage and disposal of hazardous waste	Physical inspection to ensure hazardous waste is being segregated and securely disposed off to authorised vendors	All rehabilitation worksites generating hazardous wastes	Once every month	Engineer in charge through E&S Expert
---	---	--	------------------	---------------------------------------

### 2.3.5 REPORTING

Contractor will prepare a Quarterly Progress report (QPR) and submit to Engineer in Charge. The report will cover the compliance status of the Project with the ESMP in their scope and shall include Muck/Debris Management, Resource Conservation and Pollution Prevention Plan implementation. The Engineer in Charge through E&S expert at SPMU will include its own monthly inspection report and submit the report to SPMU/IA every quarter.

## 2.4 COMMUNITY HEALTH AND SAFETY (ESS4)

### 2.4.1 OVERVIEW

Dam rehabilitation work, although limited to dam complex, can increase community exposure to risk and impacts. ESS4 addresses the health, safety, and security risks and impacts on project-affected communities and the corresponding responsibility of SPMU/IA to avoid or minimize such risks and impacts, with particular attention to people who, because of their particular circumstances, may be vulnerable. Occupational health and safety (OHS) requirements for project workers are set out in ESS2, and measures to avoid or minimize impacts on human health and the environment due to existing or potential pollution are set out in ESS3. ESDD has identified that there will not be any direct risks and impacts on communities due to proposed rehabilitation work including those who are vulnerable. Following sections propose mitigation measures in accordance with mitigation hierarchy to mitigate any indirect impact on communities

### 2.4.2 HAZARD IDENTIFICATION

Implementations of sub-project activities do not pose any community health and safety risks as the proposed rehabilitation work will be limited to dam area only. However, transportation of material; setting up of labour camp; influx of workers, though small in number and generally skilled workers only; pollution generation from rehabilitation work; may have indirect impact on community as identified in the ESDD report. The risks are summarized below:

**Traffic and Road Safety** – Sub-project activities are largely structural interventions categorised as civil works and hydro-mechanical works. This would require transportation of construction material, equipment and machinery, instrumentation, parts and accessories to the dam. In addition, there will be movement of workers (direct and contract workers) to and from site. Transportation of man and material will increase traffic on the village roads during the period of construction leading to increased risk of accidents, spillages, and noise and air emissions on generally deserted village roads.



Keeping in view the nature of proposed rehabilitation work, only few vehicles will be added per day, therefore this activity do not pose any risk to community.

**Community Exposure to Health Issues** – The sub-project activities will require contract workers – skilled and unskilled. It is expected that unskilled workers will be available locally; however, a small number of skilled workforce will come from outside the area and expected to stay at site. Influx of workers and setting up of temporary labour camp interfacing with community may increase the health risk of community. Migrant workers can be potential carriers of new infectious diseases not known in the area and impact the community health. Labour camp in vicinity of community may pose risk of unplanned waste and waste water discharge.

**Management and Safety of Hazardous Material** – Sub-project civil and hydro-mechanical interventions may require use of hazardous material in limited quantities such as fuels, flammable gases such as acetylene and LPG, etc, Transportation storage and handling of these hazardous materials requiring careful handling and disposal to minimise risk of public exposure or polluting community land and water resource.

#### **2.4.3 HAZARD RISK MANAGEMENT**

Following measures are proposed to minimise the community health and safety risks due to sub-project activities:

##### **Traffic and Road Safety**

- Transportation of loose construction material will be through covered vehicles only
- PUC for all transport vehicles will be made compulsory
- No large scale movement of vehicles at night time
- Drivers will be issued instructions to follow signage and safety norms

##### **Community Exposure to Health Issues**

- Health and hygiene requirement of the labour camp will be maintained throughout the project cycle – potable water, power, community/individual kitchen, waste management
- Separate toilets for male and female workers staying in labour camp connected to septic tanks/adequate waste collection and disposal arrangement
- Waste management system will be implemented in labour camp by providing adequate number of bins and collection system to avoid littering of waste
- Labour will be sensitized to follow good health and hygiene practices for their as well as communities health

##### **Incident Management, OHS monitoring, training:**

Labour interaction with communities, Incident prevention and management, OHS monitoring, Health and Hygiene, training are discussed as part of labour management Plan ESS2.



#### **2.4.4 COMMUNICATION AND CONSULTATION (WORKERS & COMMUNITY)**

Stakeholder consultation was carried out involving direct workers and community in the month of June 2020, during ESDD preparation. Direct workers are well aware of rehabilitation work and confirmed these activities remain limited to dam complex only. Community participants welcomed the proposed interventions relating to dam safety

and confirmed that there are no pending issues regarding dam construction related resettlement. The participants explicitly mentioned that the dam is their lifeline and strengthening works will help their long term livelihood and therefore welcomed such information. Participants have expressed that they do not have any grievances and as such no grievances were ever reported from their communities/neighbourhoods. Consultations will be continued during various phases of the project by IA.

#### **2.4.5 EMERGENCY MANAGEMENT PLAN**

Emergency Management Plan should be displayed prominently at work site in local language for ease of understanding of workers and staff. It should contain following information:

1. Name, Designation & Contact Numbers of the site supervisor and alternate to be informed in case of any emergency;
2. Contact details of nearby hospitals, fire department and police department
3. Location of fire extinguishers, first aid boxes, emergency alarm and assembly points
4. Potential Emergencies Situations such as fire, fall, electric shock, etc. & response measures such as use of fire extinguishers, rescue procedures, switching off main power (can be made pictorially)

Responsibility of site supervisor (or his alternate in case he is not present) will be clearly defined including:

1. Assess the level of emergency
2. Providing first aid/organize rescue, as per the emergency situation
3. Assess the need for hospitalization and call ambulance
4. Evacuate the area/limit entry after assessing type of emergency
5. Assess emergency situation and its potential of expanding and inform IA and first responders, as required (fire, police and medical)
6. Prepare accident report – root cause, corrective action and preventive action

#### **2.4.6 EMERGENCY CONTROL CENTRE**

Control room at dam serves as Emergency Control Centre, which has basic communication facilities. The same will be upgraded to serve as emergency control centre with following facilities:

- Display of the name of site emergency controller and all relevant phone numbers – project personnel, police, fire, medical, district administration
- Phone connection – landline/mobile (2 numbers)
- Site layout diagram with entry and exit routes / Assembly points



- Two numbers of first-aid boxes with prescribed first-aid medicines
- Two numbers of blankets
- Drinking water
- Two numbers of rescue ropes
- Two numbers of high beam torches
- Fire extinguisher of DCP and CO2 type.

#### **2.4.7 REFERENCE TO IFC ENVIRONMENTAL HEALTH AND SAFETY GUIDELINES**

The IFC guidelines of environmental health and safety provide detailed guidance note on health and safety requirement and good practices. This manual shall guide contractor and IAs while finalizing site specific contractor's EHS management plan.

### **2.5 BIODIVERSITY CONSERVATION MANAGEMENT PLAN (ESS6)**

#### **2.5.1 APPLICABILITY OF BIO CONSERVATION AND MANAGEMENT PLAN (BCMP) TO A SUB-PROJECT**

"Protected Area" means a National Park, a sanctuary, a conservation reserve or a community reserve notified under Wildlife Protection Act. Any new or expansion project within or in proximity to protected area, will have to undergo wildlife Clearance, however, rehabilitation work at existing dams in proximity to protected area do not require any clearance/compliances.

WB ESS6, "Biodiversity Conservation and sustainable Management of Living Natural Resources" requires assessing its applicability to a sub-project during ESDD, keeping in view the potential impact on biodiversity or habitat either positively or negatively, directly or indirectly.

Keeping the above in view, Biodiversity Conservation and Management Plan will be prepared for only those sub-projects which are in close proximity to any of the protected areas, to mitigate potential indirect impacts. The requirement is established during ESDD.

#### **2.5.2 SUB PROJECT DESCRIPTION**

This section will briefly describe the sub-project including activities/interventions proposed in proximity to protected area, if any.

#### **2.5.3 INVENTORY OF TERRESTRIAL AND AQUATIC FLORA FAUNA**

This section will describe the protected area and its importance with respect to terrestrial and aquatic flora and fauna species being protected.

#### **2.5.4 LIKELY IMPACT OF PROJECT ACTIVITIES ON BIODIVERSITY AREAS.**

A brief from the ESDD report about likely indirect impacts of sub-project rehabilitation work on protected area.

#### **2.5.5. CONSERVATION AND MANAGEMENT PLAN**

Following measures are proposed for conservation of biodiversity:

- Labour will be sensitized to ensure that they do not indulge in tree cutting or hunting.



- Any access/short cut, linking work sites and labour camp through PA will be blocked/fenced
- Project authorities/contractor will be bound by rules and regulation of Wildlife (Protection) Act, 1972 of India and any other rule and guidelines, stipulated by the state Government.
- No dumping site will be identified in the protected area (this is not permitted by law) and no waste dumping (even temporary) will be permitted in that area.
- The project staff and workforce will be appropriately made aware about the importance of biodiversity and shall be advised not to indulge in any illegal activity
- In case of any violation, strict action and penalties would be levied in accordance with the law by appropriate authority.

#### **2.5.6 MONITORING, COMPLIANCE REPORTING AND BUDGET**

Physical inspection by Engineer in Charge, before start of work and thereafter every month to check:

- Location of labour camp/colony wrt to conservation area and expected locations of breach
- Route of labour movement from camp/Colony to work site and back and any possible interference with the protected area (block any short cuts/access)
- Review of complaints received, if any, reporting labour movement in the protected area and take corrective action
- Review of labour training content and record to ensure labour is sensitized to the need of biodiversity conservation
- Preparing quarterly compliance report

**BIODIVERSITY CONSERVATION PLAN HAS NOT BEEN PREPARED FOR KODAYAR DAM I. SINCE IT IS NOT APPLICABLE.**

## **2.6 TRIBAL DEVELOPMENT PLAN (ESS7)**

### **2.6.1 APPLICABILITY OF TRIBAL DEVELOPMENT PLAN (TDP) TO A SUB-PROJECT**

Scheduled Areas are areas in India with a preponderance of tribal population subject to a special governance mechanism wherein the central government plays a direct role in safeguarding cultural and economic interests of scheduled tribes in the area. At present, 10 States namely Andhra Pradesh, Chhattisgarh, Gujarat, Himachal Pradesh, Jharkhand, Madhya Pradesh, Maharashtra, Odisha, Rajasthan and Telangana have Fifth Schedule Areas. Schedule VI of Article 244 (2) & Article 275 (1) of the Constitution of India makes separate arrangements for the tribal areas of Assam, Meghalaya, Mizoram, and Tripura.

Rehabilitation work proposed at sub-projects will be limited to dam area and no structural interventions are proposed outside, therefore, no direct impact on local community is assessed as part of ESDDs. The project activities do not lead to any direct or indirect impacts on local communities due to structural interventions. Only non-structural interventions such as preparation and implementation of EAP and early flood



warning systems will involve engaging with variety of stakeholders including tribal groups, living in the vicinity of the dam and would need to be consulted and informed in culturally appropriate approach – language, techniques that are familiar to them.

Tribal Development Plans will be prepared specifically for those sub-projects which fall in Schedule V and VI areas; to ensure engagement of tribal population in culturally appropriate manner during non-structural interventions.

#### **2.6.2 TRIBAL GROUPS IN THE AREA**

This section will describe the tribal groups present in the area. This should also cover the baseline data for the district - demography, occupation, etc. This should also summarise the tribal welfare programs being implemented in the area.

#### **2.6.3 PREVIOUS CONSULTATIONS**

This section will describe the stakeholder consultation carried out and concerns/observations of the local population with respect to dam rehabilitation work proposed. Any inputs specific to or from the tribal groups will be captured.

#### **2.6.4 SOCIAL IMPACTS, IF ANY**

This section will describe potential positive and negative impacts – direct or indirect, if any of the rehabilitation work on tribal population such as:

**Positive Impacts:** The tribal households will be indirectly and positively benefited by the dam safety interventions proposed for each sub-project Dam as these will help improve the overall safety of the dams.

**Potential adverse impacts:**..None

These activities in no way cause restriction on access to land or use of resources by local communities and there is no economic displacement envisaged due to the sub-project. Only non-structural interventions such as preparation and implementation of EAP and early flood warning systems will involve engaging with variety of stakeholders including tribal groups, living in the vicinity of the dam and would need to be consulted and informed in culturally appropriate approach – language, techniques that are familiar to them.

#### **2.6.5 MEASURES TO AVOID, MINIMIZE IMPACTS, IF ANY**

As the structural interventions will not lead to any adverse impacts, no specific mitigation measures are required. However, in context of non-structural measures, implementation of EAP and early flood warning system will be shared in meetings and informed in language/techniques which are conversant to them.

#### **2.6.6. FPIC**

ESS7 sets out the requirement of obtaining Free, Prior, and Informed Consent (FPIC) of affected Indigenous Peoples/ Sub-Saharan African Historically Underserved Traditional Local Communities in the three circumstances viz.

- (a) have adverse impacts on land and natural resources subject to traditional ownership or under customary use or occupation;
- (b) cause relocation of Indigenous Peoples/ Sub-Saharan African Historically Underserved Traditional Local Communities from land and natural resources



- subject to traditional owner- ship or under customary use or occupation; or
- (c) have significant impacts on Indigenous Peoples/Sub-Saharan African Historically Underserved Traditional Local Communities' cultural heritage that is material to the identity and/or cultural, ceremonial, or spiritual aspects of the affected Indigenous Peoples/ Sub-Saharan African Historically Underserved Traditional Local Communities' lives.

If any of the above three circumstance will become applicable, project risk category will change from Low to Moderate to Substantial to High. As such none of the three circumstances are found applicable and therefore, for Low to Moderate Risk project, even if it is located in Schedule V or VI areas, FPIC will not be required.

#### 2.6.7 Action Plan to be implemented with EAP

Sl.No.	Activities	Q1	Q2	Q3	Q4	Q5
1	Initial kick off meeting with communities including tribal communities on: i. project interventions including likely disruptions if any to water supply ii. Preparation of EAP including likely timelines for mapping exercises of emergency resources (e.g. boats, community volunteers, etc.) iii. Inform them of the project level GRM;					
2	For EAP preparation, • hold consultation with general tribal communities involving Sarpanch and community members • Hold separate meetings with females, disadvantaged and vulnerable groups					
3	Develop culturally appropriate IEC materials (for STs) for dissemination					
4	Disclose draft EAP at Disclosure event with participation from local villages including headmen/Sarpanch					
5	Disseminate key details (or Executive Summary) of EAP by pasting details in local villages					

**TRIBAL DEVELOPMENT PLAN HAS NOT BEEN PREPARED FOR KODAYAR DAM II. SINCE IT IS NOT APPLICABLE**

#### 2.7 CULTURAL HERITAGE PROTECTION PLAN (ESS8)

Cultural Heritage Protection Plan will be applicable to those sub-projects, where cultural heritage of significance is identified within the project area and proposed interventions may have interface with cultural heritage of the area requiring plan for heritage protection during project implementation.

ESS8 recognises that cultural heritage provides continuity in tangible and intangible forms between the past, present, and future and the CHPP is prepared for those sub projects which are likely to have risks or impacts on cultural heritage.

##### 2.7.1 SCOPE OF CULTURAL HERITAGE PROTECTION PLAN (CHPP):

CHPP shall meet the following aspects:

1. Identify the presence of Archaeological protected monuments, present in dam or close vicinity of the dam



2. Identify applicable legislative restriction and comply with them.
3. Identify physical, cultural or any religious heritage of importance to communities in the area close to or in the vicinity of dam and is/ are likely to have impact
4. Define procedure for minimising the impact if any on cultural heritage of the areas.
5. To define procedure for dealing with chance find

### 2.7.2 CHPP PREPARATION AND APPROVAL

CHPP shall be prepared prior to start of construction, by Contractor in consultation with Engineer-In-Charge in accordance with ESMF provisions.

### 2.7.3 CONTENTS OF SITE SPECIFIC CHPP

- i. **Identification of cultural resources and likely impact from the project**  
All archaeologically protected monuments and physical cultural resources of the community shall be identified. Risk and impact of the interventions on these resources shall be determined. Prior legislative permits, if applicable, shall be obtained.
- ii. **Undertake community consultation and other stakeholders consultation** so that Community consultation and evolve sustainable protection measures.
- iii. **Identification and Protection of Chance Find:**  
Any chance find of historical or archaeological importance shall be informed to authority concerned and it shall be preserved under secure conditions.
- iv. **Reporting**  
Contractor shall share the CHPP monitoring reports with Engineer-In-Charge on regular basis.
- v. **Responsibility**  
Prime responsibility of developing and implementation of CHPP shall be of the contractor. However, IA will ensure its preparation and implementation in consultation with the Contractor. The IA shall also ensure deployment of experienced Cultural Heritage expert, if required.

## 2.8 STAKEHOLDER ENGAGEMENT PLAN (ESS10)

### 2.8.1 IDENTIFICATION OF STAKEHOLDERS

Based on the current set of proposed interventions, the following potential stakeholders were identified and categorized as Affected Stakeholders, Other Interested Stakeholders, and Disadvantaged & Vulnerable Stakeholder.

- i. **Affected Persons:** There are no affected persons who shall be directly or indirectly adversely affected by the proposed interventions. It is important to also identify affected persons if gets affected from any impacts related to construction on cultural and religious heritage perspective.
- ii. **Other Interested persons:** In relation to structural interventions, these would be contractors, project management consultants, regulatory bodies/institutional stakeholders such as revenue, Pollution control board, forest and wildlife department or other environmental authorities, etc. In relation to non-structural interventions, these would be communities living downstream including farmers, village heads



(Sarpanchs), community leaders, district administration, police, state disaster management authority, revenue department, electronic and print media, etc. These communities would be key stakeholders requiring to be involved in the implementation of EAP.

- iii. **Disadvantaged and Vulnerable Stakeholders:** Illiterate persons, physically challenged, women and elderly would be key stakeholders – requiring special focus and outreach to ensure that they are well informed about the provisions of the EAP. Provide details of the stakeholder consultation meetings including outcomes.

#### **2.8.2 STAKEHOLDER ENGAGEMENT AND PROJECT CYCLE**

**Table 1** lists the different types of information, relevant target audience depending on the nature of information, modes and frequency of engagement with these stakeholders.



**Table 1 – Stakeholder Engagement by Activities**

Information to be disclosed	Target stakeholders	Tools of engagement & mode of disclosure	Frequency	Responsibility
Provisions related to a. Dam Safety b. Biodiversity around the dam and clearance if any required c. Cultural, religious or monumental heritage around dam , if exist	<ul style="list-style-type: none"> <li>✓ Contractor</li> <li>✓ SPMU staff</li> <li>✓ Forest Department</li> <li>✓ Pollution control Board</li> <li>✓ Department of culture, if required</li> <li>✓ Farmers, Communities (affected/ other interested) in the dam vicinity</li> </ul>	<ul style="list-style-type: none"> <li>✓ Consultation meetings related ESDDs and ESMP</li> <li>✓ Web disclosure of related ESDDs and ESMP</li> </ul>	<ul style="list-style-type: none"> <li>✓ Multiple</li> <li>✓ Must before work starts</li> <li>✓ During implementation</li> </ul>	SPMU
Work opportunities for ✓ Structural works ✓	<ul style="list-style-type: none"> <li>✓ Contractors</li> <li>✓ Consultants</li> </ul>	<ul style="list-style-type: none"> <li>✓ Website notifications</li> <li>✓ Tender advertisements in newspaper</li> </ul>	<ul style="list-style-type: none"> <li>✓ Multiple</li> <li>✓ Continuous</li> </ul>	SPMU
Work opportunities for ✓ Petty contracts ✓ Labor	<ul style="list-style-type: none"> <li>✓ Communities (including disadvantaged persons)</li> <li>✓ Petty contractor</li> </ul>	<ul style="list-style-type: none"> <li>✓ Meetings to inform Village heads or community representatives</li> <li>✓ Special meetings for informing tribals (Gram Sabha)</li> </ul>	<ul style="list-style-type: none"> <li>✓ Multiple</li> <li>✓ Continuous</li> </ul>	SPMU and Contractor
GBV related provisions	<ul style="list-style-type: none"> <li>✓ IA officials</li> <li>✓ Contractor personnel</li> <li>✓ Consultant personnel</li> </ul>	<ul style="list-style-type: none"> <li>✓ Office circular and training events</li> <li>✓ Website notifications</li> <li>✓ Bid documents and Contract provisions</li> </ul>	<ul style="list-style-type: none"> <li>✓ Multiple</li> <li>✓ Continuous</li> </ul>	SPMU
Labour management procedure	<ul style="list-style-type: none"> <li>✓ IA officials</li> <li>✓ Contractor personnel</li> <li>✓ Consultant personnel</li> </ul>	<ul style="list-style-type: none"> <li>✓ Website notifications</li> <li>✓ Bid documents and Contract provisions</li> </ul>	<ul style="list-style-type: none"> <li>✓ Multiple</li> <li>✓ Continuous</li> </ul>	SPMU
grievance mechanisms	<ul style="list-style-type: none"> <li>✓ Communities (affected/ other interested)</li> <li>✓ Contractors (for procurement related)</li> </ul>	<ul style="list-style-type: none"> <li>✓ Phone number or Toll free Helpline</li> <li>✓ Display boards at site with GRM information</li> <li>✓ Consultative meetings</li> <li>✓ Website notifications</li> <li>✓ Meetings to inform Village heads or community representatives</li> </ul>	<ul style="list-style-type: none"> <li>✓ Continuous</li> <li>✓ Multiple</li> </ul>	SPMU



### 2.8.3 TIMELINES FOR INFORMATION DISCLOSURE AND FEEDBACK

Information to be disclosed with timelines for providing feedback, responding to newspaper advertisements is presented below:

Table 2: Disclosure, feedback and timelines				
Disclosure of information/documents	Mode of providing feedback	Timeline for feedback	Conveying of responses by SPMU	
			No. of days	Mode
ESMF, SEF	Email id/website	-NA-		
Draft ESDDs/ESIAs; draft ESMPs	Email id/website	30 days	Within 7 days of end of feedback period	Website notification
Executive Summaries in local languages of ESMP	Email id/website	30 days	Within 7 days of end of feedback period	Website notification

### 2.8.4 MONITORING AND REPORTING

Quarterly progress reports of IA to include the following parameters

S. No.	Parameters	Status (Nos./description)
1	Number of public hearings, consultation meetings and other public discussions/forums conducted within a reporting period (e.g. monthly, quarterly, or annually);	
2	Number and types of IEC materials used	
3	Number of project events published/broadcasted in the local, regional media	
4	Type and frequency of public engagement activities;	
5	Number and type of grievances received within a reporting period (e.g. monthly, quarterly, or annually) and number of those resolved within the prescribed timeline	



## CHAPTER 3: ENVIRONMENTAL AND SOCIAL MITIGATION AND MONITORING PLAN

### 3.1 PURPOSE OF ES MITIGATION MANAGEMENT AND MONITORING

For the relevant environmental and social risks identified during the ESDD process of the Project, Management Plans are furnished in Chapter 2. This Chapter provides E&S risk/impacts mitigation and management plan, along with monitoring requirement, responsible entity for implementation of mitigation plan as well as monitoring. The mitigation measures are presented ESSwise at Table 3.1.

**Table 3.1 Environment and Social Mitigation and Management Plan**

Activity and environmental aspects	Environmental and Social Risks/Impacts	Mitigation Measures	Stage of Action	Monitoring Requirements and Frequency	Responsibility of Implementation of Mitigation Measures	Monitoring Responsibility
Labour Camp (ESS 1)	Labour health, Hygiene, Drinking Water availability and Sanitary waste generation	Provide clean, hygienic and safe camp facilities for workers with provision of safe drinking water, separate canteen facility, first aid, periodic health check-up and waste management..  Make Provision for adequate number of toilets separate for male and female, with arrangement of sewage	Before Construction	Physical Inspection by IA before construction and thereafter every 3 months or if any complaint is received whichever is earlier. Review of complaints should be done every	Contractor	IA



		collection and disposal		month by IA.		
	Water and Power requirement impacting other competitive users	Source of water and power for labour camp as per advisory from IA	Before Construction			
	Tree cutting by labour for cooking and space heating	Provision of community kitchen/kitchen fuel (LPG) for labour. Restriction of cutting any tree	Before Construction			
	Outside labour, may be bringing in new and infectious diseases not known to area	Pre deployment health check-up of labour	Before Construction	Review of records of health check-up before start of construction	Contractor	IA
	SEAH/GBV risk within as well as outside the camp	Training and awareness of workers, identification of GBV hotspots and monitoring, establishing GRM mechanism	Entire duration of project	<ul style="list-style-type: none"> <li>• Review of training records and identified GBV hotspots and monitoring arrangement at start and every 3 months</li> <li>• Monthly Review of complaints received under GRM</li> </ul>	Contractor; IA to establish GRM; GBV support	IA and SPMU for GRM
Labour employment and working conditions (ESS 2)	<ol style="list-style-type: none"> <li>1. Non-payment of wages and overtime</li> <li>2. Non-compliance to working hours, number of working days per week, rest day and rest time</li> <li>3. Inadequate facilities at site - drinking water, toilets, food</li> <li>4. Not providing temporary accommodation for labour</li> </ol>	Ensure compliance to BOCW and other applicable legal instruments; latest state government notification issued by Labour Department for minimum wages, working hours, child labour age should be complied with.	Before construction - Contractors Labour License, Insurance, ESI and PF registration	Document review such as licenses, record register and muster roll; Physical inspection of working condition at site and labour camp; every 3	Contractor	IA



	<p>free of charge with separate toilet, bathing and lavatory facilities</p> <p>5. Not providing kitchen and creche, if applicable</p> <p>6. Employment of child labour</p>		Regular review during construction	months or if any complaint is received whichever is earlier; Review of complaints received under GRM every month		
<p>Occupational Health and Safety during works</p> <p>(ESS 2)</p>	<p>1. Unsafe working conditions – poor marking, instructions,</p> <p>2. Not enough PPEs for all workers; PPEs not appropriate for all types of risks at site or Poor quality PPEs</p> <p>3. Inadequate training and awareness of workers in use of PPEs and/or in emergency response,</p>	<p>1. Contractor/Supervisor will inspect the work sites and mark them as high, moderate and low risk areas and ensure workers follow instruction to work in these areas</p> <p>2. Adequate number of good quality appropriate PPEs to be provided by contractor – helmets, gum boots, safety belts, safety harness, gloves, overalls, ear plugs, face masks, etc.</p> <p>3. All workers should be provided with training on use of appropriate PPEs and how to respond during emergency</p> <p>4. Adequate EHS instructions shall be displayed at site</p> <p>5. Provision of First aid with availability of trained first aiders shall be ensured</p> <p>6. SOP shall be developed as per best practices and</p>	<p>Before construction – training and availability of PPEs</p> <p>During construction – marking of areas as per risks, rehearsing emergency response and identify training needs</p>	<p>Review of training records, review of availability of PPEs, Review of accident records and corrective preventive action reports – before start of construction thereafter every 3 months</p>	Contractor	IA



		<p>IFC EHS guidelines for unsafe conditions like working on height, working in confined areas, electrical safety, fall prevention, handling of hazardous material like welding gases</p> <p>7. Adequate provision of life jacket if working on reservoir side</p> <p>8. Procedure of incident prevention, investigation and corrective preventive action</p>				
<p>Use of resources – water, power and raw material for dam rehabilitation work</p> <p>(ESS 3)</p>	<p>Resource wastage, impact on land environment while procuring material from quarry/borrow areas</p>	<p>Resource planning will be done by contractor in consultation with engineer in charge ( Estimate of material requirement from quarry/borrow area, identification of nearest locations with approval status . Ensure that material is sourced from quarries or borrow areas which has valid environmental clearance.</p>	<p>Before start of construction work</p>	<p>Review of resource planning ensuring efficiency Review of quarry and borrow material requirement with approval status, validity and environment clearance – once before start of construction</p>	<p>Contractor with IA</p>	<p>IA and SPMU</p>
<p>Pollution generation from rehabilitation work sites and labour camp</p>	<p>1. Air and noise emissions from storage and handling of raw material and during execution of civil and hydro-mechanical work 2. Water pollution from</p>	<p>1. Ensuring covered storage of loose material/sprinkling of water to minimize fugitive emissions 2. Maintaining construction equipment and ensuring</p>	<p>During entire project duration</p>	<p>Ambient Air Quality Monitoring only for projects which are in close proximity to</p>	<p>Contractor through NABL accredited Lab;</p>	<p>IA</p>



(ESS 3)	<p>construction activities and from labour camp</p> <p>3. Muck generation from excavation work, if any, and debris generation from repair work</p> <p>4. Hazardous waste generation from civil construction work such as painting and hydro-mechanical work, replacement of parts, etc.</p>	<p>DG set used for power have valid certificate of Type Approval and also valid certificates of Conformity of Production as per conformance labelling. DG stack height shall be as per the Consent to be obtained from State Pollution Control Board before start of work.</p> <p>3. Ensuring use of dust masks, if workers are exposed to dust emissions and ear muffs for exposure to high noise for long durations</p> <p>4. Provision of mobile toilets at work site</p> <p>5. Wastewater from construction sites not to be discharged untreated (compliance with general discharge standards)</p> <p>6. Muck and construction debris to be disposed off at pre-identified and approved site</p> <p>7. Hazardous waste (Empty barrels/containers/liners contaminated with hazardous chemicals /wastes; Contaminated cotton rags or other cleaning materials) to be separately stored and</p>		<p>protected areas (PM<sub>2.5</sub>, PM<sub>10</sub> and SO<sub>2</sub> for 24 hours) at 2 major construction sites, before start of construction (as identified by Engineer in charge) once during construction and once at the end of rehabilitation work</p> <p>Sound Level monitoring (dB(A) levels) only for projects which are in close proximity to protected areas at 2 major construction sites (as identified by engineer in charge), once before start of construction once during construction and</p>	Contractor	
---------	---	--	--	---	------------	--



		disposed off to authorised vendors only		<p>once at the end of rehabilitation work</p> <p>Monthly physical inspection to ensure wastewater from rehabilitation work is not being disposed off in river; muck/debris is being disposed off at identified locations.</p> <p>soil level : near construction camp site or active work site area where probability of waste discharge exists</p> <p>Physical inspection of use of PPEs, review of DG specification, wastewater discharge, muck and debris handling and disposal – every month</p>		
--	--	---	--	---	--	--



				Physical inspection of segregation, storage and disposal of hazardous waste to authorised vendor – every month		
Transportation of material to project site through village roads.  (ESS 4)	Increase in the traffic on village roads leading to air and noise emissions as well as risk of accidents.	1. All vehicles used by contractors for transportation of persons and material should have valid PUC 2. Loose material should only be transported in covered vehicles	During entire duration of project	Physical inspection and review of documents before construction and thereafter every 3 months or if any complaint is received whichever is earlier	Contractor	IA
Biodiversity Conservation for sub-projects in close proximity areas as per ESMP  (ESS 6)	Indirect impacts due to rehabilitation work in proximity to protected areas involving limited outside labour	1. Sensitizing labour on importance of conservation area and dos and don'ts	Before start of construction	Physical inspection of location of labour camp wrt PA before start of construction	Contractor and IA	SPMU
Tribal Development for sub-projects in Schedule V or VI	Non-structural interventions such as preparation and implementation of EAP and	During EAP Implementation: 1. Identification of scheduled areas and tribal clusters to prioritise targeting of	During implementation of EAP	Review of Plan of engagement of tribal population	IA	SPMU



areas preparing EAP (ESS 7)	early flood warning systems will involve consultation with variety of stakeholders including tribal groups, living in the vicinity of the dam and would need to be consulted and informed in culturally appropriate approach – language, techniques that are familiar to them.	<p>dispersed indigenous communities in the non-tribal areas as well as for clear targeting of tribal in the schedule V and VI areas</p> <ol style="list-style-type: none"> <li>2. Development of culturally appropriate Information Education and Communication (IEC) materials for dissemination in the project areas to avoid panic/rumours and providing correct and accurate information in a manner understood to locals</li> <li>3. Deployment of local (tribal) Community Facilitators to support awareness generation and mobilization in tribal areas.</li> </ol>		for EAP implementation Review of complaints received before start of construction		
Cultural Heritage for sub projects impacting any protected monuments as identified in ESDD (ESS 8)	Damage to monument/site of cultural heritage	<ol style="list-style-type: none"> <li>1. Before start of construction, joint inspection by contractor and IA, of cultural heritage site will be undertaken</li> <li>2. Workplan will be prepared to ensure no direct/indirect impact from work.</li> <li>3. Labour interference or labour access to the site will be prohibited</li> </ol>	Before start of construction	Review of work plan vis-à-vis protection requirement to cultural heritage Review of training records	Contractor and IA	SPMU



		<p>4. ASI rules for visit to site or any other regulation will be strictly adhered to</p> <p>5. Training and awareness of labour to cover protection of site</p>				
Stakeholder Engagement (ESS 10)	stakeholder participation, implementing the grievance mechanism, ensuring continuous information transfer through open communication	Establish grievance mechanism and implement	Before construction	Review of complaints received, if any, corrective preventive action and redressal	IA	SPMU



### 3.2 ES MITIGATION AND MONITORING PLAN – ACTION RESPONSIBILITY MATRIX

Various preparatory action and plans are to be prepared before start of construction work by contractor and Implementing Agency (Reference Chapter 2 and section 3.1) Table below lists actions to be taken by contractor and IA .

By Contractor		
Specific Action/ Preparation requirements	Reference Document /format	Stage of Action /Frequency
Preparation of Labour Camp Plan(if labour camp are proposed)	Number of workers, number of units required, duration of stay; facilities proposed to be provided – toilets, kitchen drinking water, waste management	Once - Before start of work
Health check-up of workers (if workers are planned to stay at site for more than six months)	Health check records	Once - Before start of work
Training and awareness of labour – GBV/ SEA, Code of Conduct, OHS requirements	Topics covered, date of training and attendance	First before start of work, thereafter after every 3 months
Compliance to labour laws	Copy of Labour license, ESI, PF	First before start of work, thereafter as per expiry/renewal
Identification of hazardous working locations and marking and emergency response plan	List of risky activities	Before start of work
Availability of PPEs	List of PPEs – number of each type	Before start of work
Training of workers on use of PPEs and Emergency Response	Training records	First before start of work, thereafter after every 3 months
Ambient air quality and sound level monitoring for projects in close proximity to protected areas	As per the report of NABL accredited lab	Before start of work, during construction and at the end of rehabilitation work
Identification of authorised vendor of hazardous waste	Name of the vendor, status of authorisation and copy of authorisation	Before start of work
Identification of approved quarry/borrow	Name of the supplier,	Before start of work



area	copy of approval	
Submission of Quarterly Progress Report		Within 2 weeks of end of every 3 months period from start date

By Implementing Agency supported by EMC	
Specific Action/Preparation requirements	Timeline/Frequency
Identification of suitable location of labour camp, if applicable	Before start of work
Identification of source of water and power for labour camp, if applicable	Before start of work
Identification of GBV hotspots	Before start of work
Approval of quarry/borrow area	Within one week of submission of details by contractor
Identification of ambient air quality and sound level monitoring locations for projects in close proximity to protected areas	Before start of work
Identification of muck/debris disposal location	Before start of work
Establishing GRM and its awareness - poster/signage with contact details	Before start of work
Ensuring effectiveness of GRM and review of complaints received	Every month during the entire duration of project implementation
Inspection of labour camp ensuring adequate facility	First on set up, thereafter every 3 months
Reviewing contractors documents and ensuring compliance to labour laws	First on setup, thereafter every 3 months
Ascertaining adequacy of good quality PPEs	Once before start of work, thereafter every 3 months
Physical inspection at work site - air emissions, noisy operations, use of PPEs	Every month during the entire duration of work
Submission of Quarterly Progress Report	Within one month, from end of every 3 months period from start date



## CHAPTER 4. IMPLEMENTATION ARRANGEMENTS AND ESMP BUDGET

The ESMP implementation is mainly the responsibility of Contractor engaged for the Works. Implementing Agency is responsible for Sub Project level activities not directly addressed by Contractor such as GBV referral mechanism, Stakeholder engagement etc. The EMC engaged by Implementing Agency will support the IA in implementation monitoring of ESMP.

In compliance with ESMF, the framework provisions of ESMP, which shall be implemented by Contractor will be included as part of Bids and the Contractor upon onboarding shall submit C-ESMP with updated inputs on management plans. The ESMP will be updated, should additional information/ impacts are determined during the project.

### 4.1 IMPLEMENTATION AND SUPERVISION ARRANGEMENTS

Table below outlines the management measures and implementation and supervision arrangements for the various activities at different stages of the project.

S. No	Project Stage/Activity	Management Measures	Responsibility	
			Planning and Execution	Supervision/ Monitoring
1	Establishing Labour Camp before start of construction, if required	Provision of separate toilets for male and female, sanitation and waste collection & disposal facilities, provision of kitchen fuel/community kitchen	Contractor	Engineer in Charge
2	Health check of labour before induction(in case outside labor are proposed to employ and stay for more than six months)	Health from an authorised government hospital/dispensary and submission of record	Contractor	Engineer in Charge
3	Compliance to labour laws - before start of construction	Ensure compliance to BOCW and other applicable legal instruments including; latest state government notification issued by Labour Department for minimum wages, working hours, child	Contractor	Engineer in Charge



S. No	Project Stage/Activity	Management Measures	Responsibility	
			Planning and Execution	Supervision/ Monitoring
		labour age.		
4	Identification of GBV hotspots and accident hotspots on transport route before start of construction	Physical survey and hotspot identification	E&S Expert at Dam	Engineer in Charge
5	Workers training	Workers training covering SEA/SEAH and GBV risks and consequences, OHS training and emergency actions, Code of Conduct – awareness and acceptance; biodiversity conservation	Contractor	E&S
6	Occupational Health and Safety of workers during entire duration of project	<ol style="list-style-type: none"> <li>1. Contractor/Supervisor will inspect the work sites and identify the high risk areas, if any; ensures workers follow instruction to work in these areas</li> <li>2. Adequate number of good quality appropriate PPEs to be provided by contractor – helmets, gum boots, safety belts, safety harness, gloves, overalls, ear plugs, face masks, etc.</li> <li>3. All workers should be provided with training on use of appropriate PPEs and how to respond during emergency</li> </ol>	Contractor	E&S
7	Resource planning before start of construction	<ol style="list-style-type: none"> <li>1 Resource planning will be done by contractor in consultation with engineer in charge (requirement of water and power at various location for construction work and labour camp)</li> <li>2 Estimate of material requirement from quarry/borrow area, identification of nearest locations with approval status</li> </ol>	Contractor	Engineer in Charge
8	Pollution prevention during entire project duration	<ol style="list-style-type: none"> <li>1. Ensuring covered storage of loose material/sprinkling of water to minimise fugitive emissions</li> <li>2. Maintaining construction equipment and ensuring DG set used for power have valid certificate of Type Approval and also valid certificates of Conformity of Production as per</li> </ol>	Contractor	E&S



S. No	Project Stage/Activity	Management Measures	Responsibility	
			Planning and Execution	Supervision/ Monitoring
		conformance labelling 3. Ensuring use of dust masks, if workers are exposed to dust emissions and ear muffs for exposure to high noise for long durations 4. Provision of mobile toilets at work site 5. Wastewater from construction sites not to be discharged untreated (compliance with general discharge standards) 6. Muck and construction debris to be disposed off at pre-identified and approved site 7. Hazardous waste (Empty barrels/containers/liners contaminated with hazardous chemicals /wastes; Contaminated cotton rags or other cleaning materials) to be separately stored and disposed off to authorised vendors only		
9	Safe transportation of man and material during entire duration of project	1. All vehicles used by contractors for transportation of persons and material should have valid PUC 2. Loose material should only be transported in covered vehicles 3.	Contractor	Engineer in Charge
10	Inspection of Labour Camp wrt to Conservation Reserve	1. Physical inspection ensuring no easy access to conservation reserve from work site/labour camp and shortcuts 2. Blocking of access/shortcuts 3.	E&S Experts	Engineer in Charge
12	EHS monitoring	To be undertaken throughout the project implementation period with inspection by E& S staff of contractor monthly and report submission	E&S experts of contractor	IA



### **Reporting by contractor and monitoring by SPMU**

Contractor will prepare a Quarterly Progress report (QPR) and submit to E&S Experts/SPMU giving the compliance of ESMP. Details will include status on:

1. Progress on ESMP implementation work plan
2. Status of Compliance with E&S statutory requirements such as labour licenses, insurance, etc.
3. ESHS incidents & supervision
4. Usage (no. required, distributed and used) of Personal Protective Equipment (PPE) such as hard hats, safety shoes and safety vests by workers
5. Safety at work sites like incidents, providing traffic signage, barriers/delineator, management of traffic, drainage and pliable road surface etc.
6. Training conducted, and worker's participation (submit reports with statistics of training and worker's participation)
7. Functioning of GRM relating to labour aspects, including summary details of Workers grievances, if any
8. Community grievances, if any
9. Corrective Actions and planned E&S activities for next quarter

SPMU will prepare its quarterly monitoring report and submit the same along with contractors report to CPMU.



## **ANNEXURE 1: OUTLINE OF CONTRACTOR'S ESMP**

**(Will cover all on site issues and responsibility with management; include chance find procedure if applicable)**

- 1. Sub-project activities description under Contractor's Scope**
- 2. Licensing Requirement**
  - 2.1 Labour License
  - 2.2 Insurance
  - 2.3 Use of approved quarry/borrow areas, if such material is required
  - 2.4 Any other
- 3. Workforce management under COVID 19 considerations, if applicable**  
**Refer Annexure 9.**
- 4. Labour Camp (if outside labour is accommodated in a labour camp)**
  - 4.1. Location of Labour Camp
  - 4.2. Number of labour to be housed and duration
  - 4.3. Break-up of labour workforce – male, female, children
  - 4.4. Number of Units in Labour Camp
  - 4.5. Source and Provision of Water and Power Connection including Drinking Water
  - 4.6. Cooking Arrangement – Individual Kitchen/community Kitchen
  - 4.7. Source, Type and Provision of Kitchen Fuel
  - 4.8. Toilet facilities – individual/community; fixed/mobile and sewage disposal arrangement
  - 4.9. Waste collection and disposal arrangement
  - 4.10. Identify Risk of Community Interface – any fencing/separation requirement
  - 4.11. Security and general lighting arrangement
- 5. Resource Planning**
  - 5.1. Water and power requirement for works and locations
  - 5.2. Need for water line or electrical wiring
  - 5.3. Raw material requirement and source(s)
  - 5.4. Temporary storage(s) at site and location(s) – cover/uncovered
  - 5.5. Transportation route from source to storage
- 6. Pollution Prevention**
  - 6.1. Potential of dust emission from openly stored raw material and mitigation arrangement – covering, sprinkling, etc.



- 6.2. Potential of water pollution from spillage and leakage from raw material storage and preventive measures
- 6.3. Potential of air emissions from works including toxic emissions from paints and chemicals, emissions from DG sets and other construction equipment – locations where potential is high, possibility of community impact, impact on workers, preventive measures such as dust masks for workers, etc.
- 6.4. Potential of noise generation from works (use of equipment and machinery, demolition work) including from any activity planned at night time – locations where potential is high, possibility of community impact, impact on workers, preventive measures such as ear muffs, etc.
- 6.5. Potential of water pollution from works – possibility of leakage to surface water or accumulation in low lying areas; preventive measures/treatment requirement
- 6.6. Estimate of excavated earth/construction debris requiring disposal – quantum, sources(s) of generation, identified dumping sites, transportation mode and route, period of dumping and restoration plan

**7. Occupation Health & Safety and Emergency Management**

- 7.1. PPE requirement and numbers
- 7.2. Lists of tasks and work zone critical for hazard prevention, if any
- 7.3. Location of warning signage for hazard prevention
- 7.4. Requirement of first aid boxes and portable fire extinguishers
- 7.5. Key person(s) to be contacted during emergency
- 7.6. Protocol for deciding the level of emergency – need for hospitalization, information to authorities, etc.
- 7.7. Process of accident analysis, corrective and preventive measures and need for reporting

**8. Addressing GBV Risks**

- 8.1 Preventive measures – provision of lighting, separate toilet areas for men and women, increased vigil and security arrangement for community sensitive GBV hotspots, if identified by dam authorities.
- 8.2 Sensitizing and awareness of labour on GBV issues including penalties and legal action against offenders
- 8.3 Awareness about GRM

**9. Code of Conduct**

- 9.1 Preparation of Code of conduct
- 9.2 Making labour aware of conduct with all the provisions, do's and don'ts, penalties for non-compliances, etc.
- 9.3 Displaying CoC at prominent locations



9.4 Signing of CoC by workers

**10. Awareness and Training**

10.1 Plan for training and awareness covering Pollution Prevention, OHS, Use of PPEs, Accident reporting and emergency management, CoC, GBV, GRM, etc.

10.2 Training schedule

10.3 Training records



## **ANNEXURE 2: SUB-PROJECT SPECIFIC E&S SENSITIVE INFORMATION**

The Kodayar dam I is located across the river Kodayar in the Kanyakumari district in the state of Tamil Nadu. The proximity villages' areas i.e. villages which fall within 5 km distance from the dam, are Kadambanmoodu,,Kalial and Pechiparai. There are no Schedule V<sup>1</sup> areas in state of Tamil Nadu. The district is divided into six revenue Divisions namely Thovalai, Agastheeswaram, Kalkulam, Killiyur, Thiruvattar, and vilavancode.

Kanyakumari District is a land of varied topography with sea on three sides and the mountains of the western Ghats bordering the northern side. The district comprises of four out of the five traditional land classifications namely the Kurunchi, Mullai, Marutham and Neidhal. The district also represents a varied cropping pattern from Rice being cultivated in Yela condition to Tea and coffee cultivated in higher elevations. The district has a unique advantage of rainfall during both the south west and north east monsoons. Kanyakumari District extends over a geographical area of 1,67,200 Hectares with net sown area of 74,712 Hectares which accounts for 44.6 percent of the total area.: Paddy is the main food crop in the district. It is grown in two seasons. April – June (Kannipoo) and September – October (Kumpapoo). Pulses are raised as rice-fallows. Blackgram is the main pulse crop. Coconut is a major plantation crop, cultivated extensively in this district. The soil pH is between 4.5 to 8.0.

The Agricultural Department plays major role in improving the livelihood of farmers. Various centrally sponsored and state schemes are being implemented in the district to enhance sustainable development and increase production

The economy of the district is basically dependent on non-agricultural activities & resources. A large number of tea processing industries are the major employment generation for the local people in the district. The brief demographic characteristic of the district is given in the table below:



<b>No. of Households</b>	<b>4,82,175</b>	<b>Household Size</b>	
<b>Total Population</b>	<b>18,70,374</b>	<b>Population (0-6 age)</b>	<b>182,350</b>
Male	9,26,345	Boys (0-6 age)	92,835
Female	9,44,029	Girls (0-6 age)	89,515
Sex Ratio	1019	Sex Ratio (0-6)	964
<b>Population (SC)</b>	<b>74,249</b>	<b>Population (ST)</b>	<b>7,282</b>
Male	36,817	Male	3,554
Female	37,432	Female	3,728
<b>Literates</b>	<b>15,48,738</b>	<b>Literacy Rate</b>	<b>91.75</b>
Male	780,541	Male	93.65
Female	768,197	Female	89.90
<b>No. of Workers</b>	<b>6,79,620</b>	<b>Cultivators</b>	15,610(2.30%)
Male	5,24,629	<b>Agricultural Labours</b>	72,867(10.72%)
Female	1,54,991	<b>Household Industrial Workers</b>	35,789(5.27%)
<b>No. of Main Workers</b>	<b>5,52,658</b>	<b>Other Workers</b>	5,55,354(81.72%)
<b>No. of Marginal Workers</b>	<b>1,26,962</b>		
<i>Source: Census of India, 2011 (District Handbook)</i>			

Schedule tribe population in the district is very limited and are scattered. There are only very few Scheduled Tribe households in the downstream areas and they are mainstreamed in the area with other households. No physical interventions planned in the downstream areas.



## ANNEXURE 3: SAMPLE CODE OF CONDUCT (COC)

(Translate to local language also)

### **Code of Conduct**

1. I will comply with applicable national and company laws, policies, rules, and regulations (including policy on sexual harassment).
2. I will Compliance with applicable health and safety requirements to protect the local community (including vulnerable and disadvantaged groups), the employer's personnel, and the contractor's personnel (including wearing prescribed personal protective equipment, preventing avoidable accidents and a duty to report conditions or practices that pose a safety hazard or threaten the environment).
3. I Will not use illegal substances.
4. I Will not discriminate in dealing with the local community and all co-workers. I will Treat women, children (persons under the age of 18), and men with respect regardless of race, colour, language, religion, political or other opinions, national, ethnic or social origin, property , disability, birth or other status.
5. I Will not indulge in sexual harassment (for example prohibition of the use of language or behaviour particularly towards women and/or children, that is inappropriate, abusive, sexually provocative, demeaning or culturally inappropriate)
6. I will not involve violence, including sexual and/or gender-based violence (for example acts that inflict physical, mental or sexual harm or suffering, threats of such acts, coercion, and deprivation of liberties).
7. I Will not mix/interact with children (anyone under the age of 18), and ensure their safety in the project areas.
8. I will adhere to Sanitation requirements (for example, to ensure workers use specified sanitary facilities provided by their employer).
9. I will Avoid conflict of interest(such that benefits, contracts, or employment, or any sort of preferential treatment or favours, are not provided to any person with whom there is a financial, family or personal connection).
10. I will Respect reasonable work instructions (including environmental and social norms).
11. I will adhere to Protection and proper use of property (for example, to prohibit theft, carelessness or waste).
12. I Will attend training for the duration of the contract for understanding this code of conduct.
13. I Will report violations of this code. All staff must report suspected or actual violations by a fellow worker, whether in the same contracting firm or not. Reports must be made through the GRM setup for this purpose.
14. I know that Sanctions may be applied if an employee is confirmed to be a gender-based violence perpetrator. (The sanctions will be proportional to the transgression and in accordance with applicable laws and policies).
15. I know that Non-retaliation against workers who report violations of the code, if that report is made in good faith.

I have read and was explained all the contents given above, and I understand the requirement. I shall strictly adhere to this code of conduct in all the areas of work. I understand the insistence on compliance with these norms which are mandatory for me.

Name:

Signature



### நடத்தைவிதி (Code of Conduct)

1. பொருந்தக்கூடியதேசியமற்றும்நிறுவனசட்டங்கள், கொள்கைகள், விதிகள்மற்றும்ஒழுங்குமுறைகள் (பாலியல்துன்புறுத்தல்தொடர்பானகொள்கைஉட்பட) ஆகியவற்றுடன்இணங்குதல்.  
Compliance with applicable national and company laws, policies, rules, and regulations (including policy on sexual harassment).
2. உள்ளூர்சமூகம் (பாதிக்கப்படக்கூடியமற்றும்பின்தங்கியகுழுக்கள்உட்பட), முதலாளியின்பணியாளர்கள்மற்றும்ஒப்பந்ததாரரின்பணியாளர்கள் (பரிந்துரைக்கப்பட்டதனிப்பட்டபாதுகாப்புஉபகரணங்களைஅணிவது, தவிர்க்கக்கூடியவிபத்துகளைத்தடுப்பதும்நிலைமைகள்அல்லது நடைமுறைகளைப்புகாரளிப்பதுஉட்பட) பொருந்தக்கூடியசுகாதாரமற்றும்பாதுகாப்புத்தேவைகளுக்குஇணங்கு தல். பாதுகாப்புஆபத்துஅல்லதுசுற்றுச்சூழலுக்குஅச்சுறுத்தல்).  
Compliance with applicable health and safety requirements to protect the local community (including vulnerable and disadvantaged groups), the employer's personnel, and the contractor's personnel (including wearing prescribed personal protective equipment, preventing avoidable accidents and a duty to report conditions or practices that pose a safety hazard or threaten the environment).
3. சட்டவிரோதபொருட்களைபயன்படுத்தமாட்டோம்.  
Will not use illegal substances.
4. உள்ளூர்சமூகத்துடனும்அனைத்துசகஊழியர்களுடனும்கையாள்வதில் பாரபட்சம்காட்டமாட்டார்கள். இனம், நிறம், மொழி, மதம், அரசியல்அல்லதுபிறகருத்துக்கள், தேசிய, இனஅல்லதுசமூகதோற்றம், சொத்து, ஊனம், பிறப்புஅல்லதுபிறஅந்தஸ்துஆகியவற்றைப்பொருட்படுத்தாமல்பெண் கள், குழந்தைகள் (18 வயதுக்குட்பட்டவர்கள்) மற்றும்ஆண்களைமரியாதையுடன்நடத்துங்கள்.  
Will not discriminate in dealing with the local community and all co-workers. Treat women, children (persons under the age of 18), and men with respect regardless of race, colour, language, religion, political or other opinions, national, ethnic or social origin, property, disability, birth or other status.
5. பாலியல்துன்புறுத்தலில்ஈடுபடமாட்டோம் (உதாரணமாக, மொழிஅல்லதுநடத்தையைப்பயன்படுத்துவதைத்தடைசெய்தல், குறிப்பாகபெண்கள்மற்றும்/அல்லதுகுழந்தைகளிடம், இதுபொருத்தமற்ற, தவறான, பாலியல்துண்டுதல், இழிவுபடுத்தும்அல்லதுகலாச்சாரரீதியாகபொருத்தமற்றது).  
Will not indulge in sexual harassment (for example prohibition of the use of language or behaviour particularly towards women and/or children, that is inappropriate, abusive, sexually provocative, demeaning or culturally inappropriate).
6. பாலியல்மற்றும்/அல்லதுபாலினஅடிப்படையிலானவன்முறைஉட்படஎ ந்தவன்முறையும்இல்லை (உதாரணமாக, உடல், மனஅல்லதுபாலியல்பாதிப்புஅல்லதுதுன்பத்தைஏற்படுத்தும்செயல்க



மனஅல்லதுபாலியல்பாதிப்புஅல்லதுதுன்பத்தைஏற்படுத்தும்செயல்கள், அத்தகையசெயல்களின்அச்சுறுத்தல்கள், வற்புறுத்தல்மற்றும்சுதந்திரத்தைபறித்தல்).

No violence, including sexual and/or gender-based violence (for example acts that inflict physical, mental or sexual harm or suffering, threats of such acts, coercion, and deprivation of liberties).

7. பாலியல்சுரண்டல்மற்றும்துஷ்பிரயோகம்உட்படஎந்தசுரண்டலும்இல்லை (உதாரணமாகபாலினத்திற்காகபணம், வேலை, பொருட்கள்அல்லதுசேவைகளைபரிமாற்றம்செய்வதைதடைசெய்தல், பாலியல்சலுகைகள்அல்லதுபிறஅவமானங்கள், இழிவானநடத்தை, சுரண்டல்நடத்தைமற்றும்அதிகாரதுஷ்பிரயோகம்உட்பட).

No exploitation including sexual exploitation and abuse (for example the prohibition of the exchange of money, employment, goods or services for sex, including sexual favours or other forms of humiliation, degrading behaviour, exploitative behaviour, and abuse of power).

8. 18 வயதிற்குட்பட்டஎவருடனும்உடலுறவில்ஈடுபடுவதைத்தவிர்க்கவும், மேலும்இந்தகுறியீட்டைமீறினால்வேலைவாய்ப்பைப்பாதிக்கக்கூடியதடைகள்விதிக்கப்படும்.

Refrain from sex with anyone under the age of 18 and that the breach of this code will incur sanctions that could impact employment.

9. குழந்தைகளுடன் (18 வயதுக்குட்பட்டஎவரும்) கலக்கவோ/ஊடாடவோகூடாது, மேலும்திட்டப்பகுதிகளில்அவர்களின்பாதுகாப்பைஉறுதிசெய்யும். Will not mix/interact with children (anyone under the age of 18), and ensure their safety in the project areas.

10. சுகாதாரத்தேவைகள் (உதாரணமாக, தொழிலாளர்கள்தங்கள்முதலாளிவழங்கியகுறிப்பிட்டசுகாதாரவசதிகளைப்பயன்படுத்துவதைஉறுதிசெய்ய). Sanitation requirements (for example, to ensure workers use specified sanitary facilities provided by their employer).

11. வட்டிமுரண்பாட்டைத்தவிர்க்கவும் (நிதி, குடும்பம்அல்லதுதனிப்பட்டதொடர்புஉள்ளஎந்தவொருநபருக்கும்நன்மைகள், ஒப்பந்தங்கள்அல்லதுவேலைவாய்ப்பு, அல்லதுஎந்தவகையானமுன்னுரிமைசிகிச்சைஅல்லதுசலுகைகள்வழங்கப்படாது).

Avoid conflict of interest(such that benefits, contracts, or employment, or any sort of preferential treatment or favours, are not provided to any person with whom there is a financial, family or personal connection).

12. நியாயமானபணிவழிமுறைகளை (சுற்றுச்சூழல்மற்றும்சமூகவிதிமுறைகள்உட்பட) மதிக்கவும். Respect reasonable work instructions (including environmental and social norms).

13. சொத்துபாதுகாப்புமற்றும்முறையானபயன்பாடு (உதாரணமாக, திருட்டு, கவனக்குறைவுஅல்லதுகழிவுகளைதடைசெய்ய). Protection and proper use of property (for example, to prohibit theft, carelessness or waste).

14. இந்தநடத்தைநெறிமுறைகளைப்புரிந்துகொள்வதற்கானஒப்பந்தத்தின் காலத்திற்கானபயிற்சியில்கலந்துகொள்வார். Will attend training for the duration of the contract for understanding this code of conduct.



விட்டாலும்,

சுகதொழிலாளியின்சந்தேகத்திற்குரியஅல்லதுஉண்மையானமீறல்களைப்புகாரளிக்கவேண்டும். இந்தநோக்கத்திற்காக GRM அமைப்புமூலம்அறிக்கைகள்செய்யப்படவேண்டும்.

Will report violations of this code. All staff must report suspected or actual violations by a fellow worker, whether in the same contracting firm or not. Reports must be made through the GRM setup for this purpose.

16. ஒருபணியாளர்பாலினஅடிப்படையிலானவன்முறைகுற்றவாளிஎனஉறுதிசெய்யப்பட்டால், தடைகள்விதிக்கப்படலாம். தடைகள்மீறலுக்குவிகிதாசாரமாகவும்பொருந்தக்கூடியசட்டங்கள்மற்றும்கொள்கைகளின்படியும்இருக்கும்.

Sanctions may be applied if an employee is confirmed to be a gender-based violence perpetrator. The sanctions will be proportional to the transgression and in accordance with applicable laws and policies.

17. அந்தஅறிக்கைநல்லெண்ணத்துடன்செய்யப்பட்டால், குறியீடுமீறல்களைப்புகாரளிக்கும்தொழிலாளர்களுக்குஎதிராகப்பழிவாங்கப்படாது.

Non-retaliation against workers who report violations of the code, if that report is made in good faith.

மேலேகொடுக்கப்பட்டுள்ளஅனைத்துஉள்ளடக்கங்களையும்நான்படித்துவிளக்கியுள்ளேன்,

மேலும்தேவையைப்புரிந்துகொண்டேன்.பணியின்அனைத்துபகுதிகளிலும்இந்தநடத்தைநெறிமுறைகளைநான்கண்டிப்பாககடைபிடிப்பேன். எனக்குகட்டாயமாகஇருக்கும்இந்தவிதிமுறைகளுக்குஇணங்கவேண்டுமென்றவலியுறுத்தலைநான்புரிந்துகொள்கிறேன்.

I have read and was explained all the contents given above, and I understand the requirement. I shall strictly adhere to this code of conduct in all the areas of work. I understand the insistence on compliance with these norms which are mandatory for me.

பணியாளர்களின்பெயர்:

ஒப்பந்ததாரரின்பெயர்:



## **ANNEXURE 4:**

### **Grievance Redressal Mechanism (SAMPLE)**

**DAM REHABILITATION AND IMPROVEMENT PROJECT**  
**(DRIP) PHASE II & III**  
**(UNDER WORLD BANK FUNDING AND SUPERVISION CENTRE WATER COMMISSION)**

**Name of work :** Dam Rehabilitation and Improvement Works to Kodayar Dam – I n Tirunelveli Generation Circle, Tamil Nadu Under DRIP - II.

**Name of Contractor :**

**Agreement No :**

**List of works**

**CIVIL WORKS:**

1. Grouting the leakage holes with polyurethane and surface treatment with micro-concrete inside the regular gate groove.
2. Replacing the worn out slanting pumping water pipe portion with new with required anchoring arrangement.
3. Repairing the scoured bottom of the left side abutment and Pier foundation by constructing a skin wall.
4. Reaming the vertical shafts, providing caps to the vertical shafts, cleaning the entire dam masonry for saddle dam 1 & 2.
5. Raking and pointing works in u/s masonry joints to reduce the abnormal seepage observed from the transverse gallery duct for saddle dam 1 & 2.
6. Clearing the approach ways and provide concrete to enable periodical inspection and maintenance of the saddle dams.
7. Cutting of the damaged T-guides and replacing the same with suitable corrosion resistant material and fixing the same with wall fasteners and grouting method without disturbing the second stage concrete.

**FOR ANY GRIVANCE CONTACT:**

Er.P.Rameshwari,

Executive Engineer/Civil/ DRIP/ Madurai 94454 42372


Er.J.Nagarajan,

Executive Engineer/ Civil/ DRIP/ Chennai 94437 83931



## **ANNEXURE 5: INTERNAL COMPLAINT'S COMMITTEE (SAMPLE)**

### **GREIVENCE REDRESSAL MECHANISM (GRM)/INTERNAL COMPLIANCE COMMITTEE (ICC)**

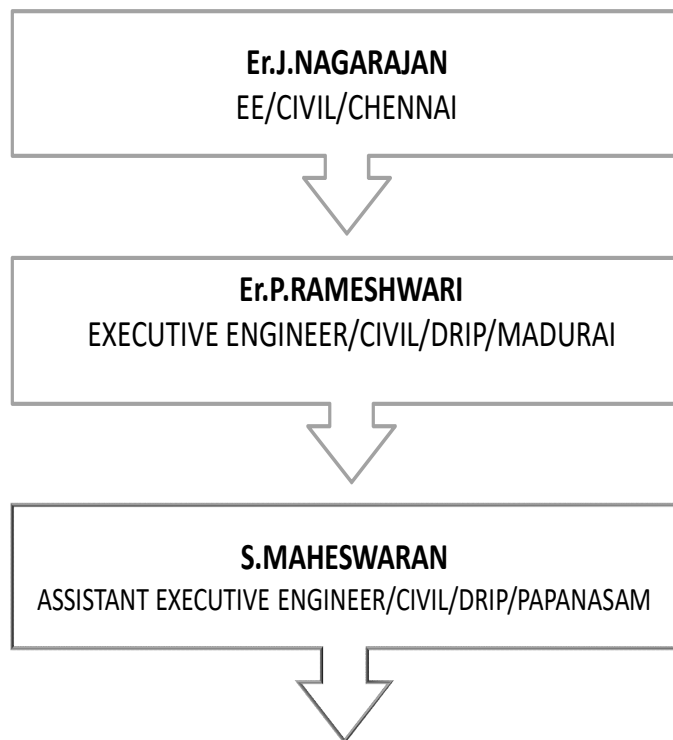








## **CONTRACTOR'S GRM COMMITTEE (SAMPLE)**



## ANNEXURE 6: STANDARD OPERATING PROCEDURE (SOP)

WORK AT HEIGHTS உயரத்தில் வேலை	WELDING AND CUTTING OPERATION வேல்டிங் மற்றும் கட்டிங் ஆபரேஷன்	ELECTRICAL SAFETY மின் பாதுகாப்பு	EXCAVATION WORK குழி வேலை	HANDLING OF HAZARDOUS CHEMICALS ஆபாயகரமான இரசாயனங்களை கையாள்தல்
1 Be trained to work at heights	1 Hoses shall be in good condition.	1 Work shall be done by qualified, experienced electrical technicians.	1 Proper inspection shall be done to identify underground utility services existing near or inside the excavation areas.	1 Hazardous chemicals shall be stocked safely at the site.
உயரத்தில் வேலை செய்பவர்கள் பயிற்சி பெற்றவர்கள்	குழாய்கள் தலைய நிலையில் இருக்க வேண்டும்	தகுதி வாய்ந்த, அனுபவம் வாய்ந்த மின் தொழில்நுட்ப வல்லுனர்கள் வேலை செய்பவர்கள் வேண்டும்.	குழி வேலை பகுதிகளுக்கு அருகில் அல்லது உள்நிலை இருக்கும் நிலைத்துப் பாய்ச்சலுக்கு சேதமடைகின்ற அமைப்புகளை அல்லது பாதுகாப்பு கருவிகளை அடையாளம் காணும் முறைப்பாடு அமல்படுத்தப்பட வேண்டும்.	ஆபாயகரமான இரசாயனங்கள் தூதத்தில் பாதுகாப்பாக சேமிக்கப்பட வேண்டும்.
2 Install full edge protection	2 Hoses shall not be wrapped around cylinders	2 All electrical installations shall be checked periodically, shall be free from short circuit, loose contacts, insulation failure etc.	2 All excavated areas shall be cordoned off with barriers of minimum height 2.5 m and tape, to prevent public access.	2 Material safety data sheet (MSDS) shall be readily available at the project site.
முழு விளிம்பு பாதுகாப்பு அமைப்பை நிறுவுதல்	சிலிண்டர்கள் சுற்றி குழாய்களை மூடக்கூடாது	அனைத்து மின் நிறுவனங்களும் அல்லது மின் சுரங்கங்களும் உடனடி, குறுகிய காலம், தாமதமான தொடர்புகள், சுட்டிப் பெய்தல் போன்றவற்றிலிருந்து விடுபட்டிருக்க வேண்டும்.	குழி வேலை செய்பவர்கள் அனைத்து பகுதிகளுக்கும் குறைந்தது குறைந்தது 2.5 மீட்டர் உயரம் கொண்ட தாதுகளை மூலம் கட்டுவதற்கான திட்டம் வகுக்கப்பட வேண்டும்.	மொதல் பாதுகாப்பு தரவு தகவல் (MSDS) திட்ட தளத்தில் உடனடியாகக் கிடைக்கிறது.
3 Barricade danger area	3 Regulators shall be checked for leaks.	3 Work on live lines must be avoided.	3 Excavated material shall be deposited clear of the trench to avoid the fall of debris.	3 Safety signs, symbols, and cautionary instructions shall be displayed.
பேரிகேட் ஆபத்து பகுதி	ஒவ்வொரு குழாய்க்கு லீக்கைகள் உள்ளதா என்பதை சரிபார்க்கப்பட வேண்டும்.	வீதாடி வரிகளில் வேலை தவிர்க்கப்பட வேண்டும்	3. குப்பைகள் விலகலுடன் தனிப்படுத்தலாக ஆய்விதரவுகள் கொடுக்கப்பட வேண்டும். அருகில் இருந்து தொலைவில் வைக்க வேண்டும்.	எச்சரிக்கை வழிமுறைகள் காட்டப்படும்.
4 Don't use unsafe platforms	4 Arrestor must be fitted in supply line from the cylinder/generator to the burner.	4 Use PPE such as rubber hand gloves, rubber shoes, etc.	4 Excavators shall be operated by licensed drivers only.	4 Provide PPE such as gloves, goggles etc.
பாதுகாப்பு அல்லாத தளத்தைப் பயன்படுத்த வேண்டாம்	சுரங்கத்தின் வழியாக வழங்கப்படும் வாயுவைப் பிடித்துக்கொள்ளும் வாயுவைப் பிடித்துக்கொள்ள வேண்டும்.	4. ஏதாவது கையுறைகள், ஏதாவது காலணிகள் போன்ற பாதுகாப்புப் பொருட்களைப் பயன்படுத்த வேண்டும்.	குழி வேலை இயக்குபவர்கள் உரிம பெற்ற ஓட்டுநர்கள் மட்டுமே இயக்கப்பட வேண்டும்.	கையுறைகள், கண்ணாடிகள் போன்ற PPE ஐ வழங்க வேண்டும்.
5 Harness work tools	5 Ensure adequate ventilation while doing welding & cutting operations in confined areas.	5 Danger notice and other safety instructions & signs should be displayed near electrical installations.	5 Relevant PPE such as hard hats, safety boots, goggles, ear protectors and glove shall be used.	
ஹார்னஸ் வேலை கருவிகள்	வேல்டிங் செய்யும் போது போதுமான காற்றோட்டத்தை உறுதி செய்து கொள்ள வேண்டும்.	ஆபத்து அறிவிப்பு மற்றும் பிற பாதுகாப்பு வழிமுறைகள்	கடினமான தொண்டிகள், பாதுகாப்பு மூச்சு, கண்ணாடிகள், காது பாதுகாப்பு கருவிகள் மற்றும் கைகளை பாதுகாப்பு தொண்டி PPE பயன்படுத்தப்பட வேண்டும்.	
	6 Personal protective Equipment (PPE) shall be used		6 Warning signs shall be provided around the cordoned area.	
	தனிப்பட்ட பாதுகாப்பு உபகரணங்கள் (PPE) பயன்படுத்தப்பட வேண்டும்		கட்டுவதற்கான பகுதிக்குள் கட்டுவதற்கான எச்சரிக்கைப் பலகைகள் வைக்கப்பட வேண்டும்.	
				



## ANNEXURE 7: SAFETY SIGNS

**தனிப்பட்ட பாதுகாப்பு உபகரணம்**

பாதுகாப்பு கவசம்	
காது ப்ளக்/ கழுத்து பட்டி	
எல்லாவற்றையும் மூடு	
பாதுகாப்பு காகிள்கள்	
கை பாதுகாப்பு	
பாதுகாப்பான காலனிகள்	

உங்களது பாதுகாப்பிற்காக எப்போதுமே உங்கள் பாதுகாப்பு உபகரணங்களை அணிந்துகொள்ளவும்

**கவனி. யோசி. செய்.**

கம்பீர இயக்கம் என வாரியர்கள் உபகரணங்களை மறந்து கொண்டு வர போகிறார்கள் உபகரணங்களை மறந்து கொண்டு வர போகிறார்கள்

### 6 கூரைகளில் வேலை செய்வதற்கான அடிப்படை வேலையிடப் பாதுகாப்பு, சுகாதார (WSH) விதிமுறைகள்

கூரைகளில் வேலை செய்பது அதிக ஆபத்தானது. கூரைகளில் வேலை செய்பது போன்ற காரணங்களால் கால்கள் அல்லது மூலம் நேரடியாக ஓய்வோர் ஆகலாம். கூரைகளில் வேலை செய்பது 2 மீட்டர் உயரத்தில் மூலம் வேலை செய்பது 21 மீட்டர் உயரத்தில் வேலை செய்பது போன்ற காரணங்களால் கால்கள் அல்லது மூலம் நேரடியாக ஓய்வோர் ஆகலாம்.

உங்களுக்கு உடல் நலமில்லாவிட்டால் மேலதிகாரியிடம் தெரியப்படுத்துங்கள்.

கூரை பணிகளுக்கு முறையான நுழைவுமையையும் வெளிவழியையும் பயன்படுத்துங்கள்.

கூரை ஓரத்தில் சுற்றத்தடுப்புக் கம்பிகள் போன்ற பாதுகாப்பு இருக்கிறதா என்பதை உறுதிப்படுத்துங்கள்.

உயரத்தில் வேலை செய்யும்போது பாதுகாப்பு வார/கவசம் அணியுங்கள்.

உடையக்கூடிய கூரை மேற்பரப்புகளில் மிதிக்காதீர்கள்.

திறப்புகள் இருக்கிறதா என கவனியுங்கள்.





## Potential Hazards

Electrical Shocks Head Impacts Splashes, Spills & Drips



- accidents result in shocks and burns



- falling or flying objects cause sprains, fractures, and concussions



- materials can irritate and burn eyes and skin



## 10 SIMPLE CONSTRUCTION SITE SAFETY RULES

Every year thousands of people are injured on construction sites. Follow these rules and stay safe.

### 1 ALWAYS WEAR PPE

PPE is your last line of defence against danger. It protects you if something goes wrong, and helps make sure you are seen. Wear it.



### 2 GET YOUR INDUCTION

Make sure you know what is happening on site so you can work safely. Your induction is important, don't start without one.



### 3 BE TIDY

Construction work is messy. Keep your work area tidy to reduce the risk of trips and slips, and fire hazards. Keep access routes clear.

### 4 ACT SAFE

Construction sites are dangerous places to work. Think safe and act safe throughout your shift.

### 5 FOLLOW SIGNS

Follow signs and procedures. Check risk assessments and systems of work. Control measures are put in place for your safety.



### 6 DO NOT ENTER

Never work in unsafe areas. Don't work at height without suitable fall prevention. Don't enter unsupported trenches. Don't work below crane loads or other dangerous operations.

### 7 REPORT

If you notice a problem, don't ignore it, report it to your supervisor immediately.

### 8 DON'T TAMPER

Never remove guard rails or scaffold ties. Do not remove guards. Do not attempt to fix defective equipment unless you are competent to do so. Do not ever tamper with equipment without authorisation.


### 9 USE THE RIGHT EQUIPMENT

Use the right equipment for the task. Check and test for defects before use. Use 110V equipment only, suitable for use on a construction site.



### 10 IF IN DOUBT, ASK

Better safe than sorry. Mistakes on construction sites can cost lives - don't let it be yours. If you need help or further information speak to your supervisor.

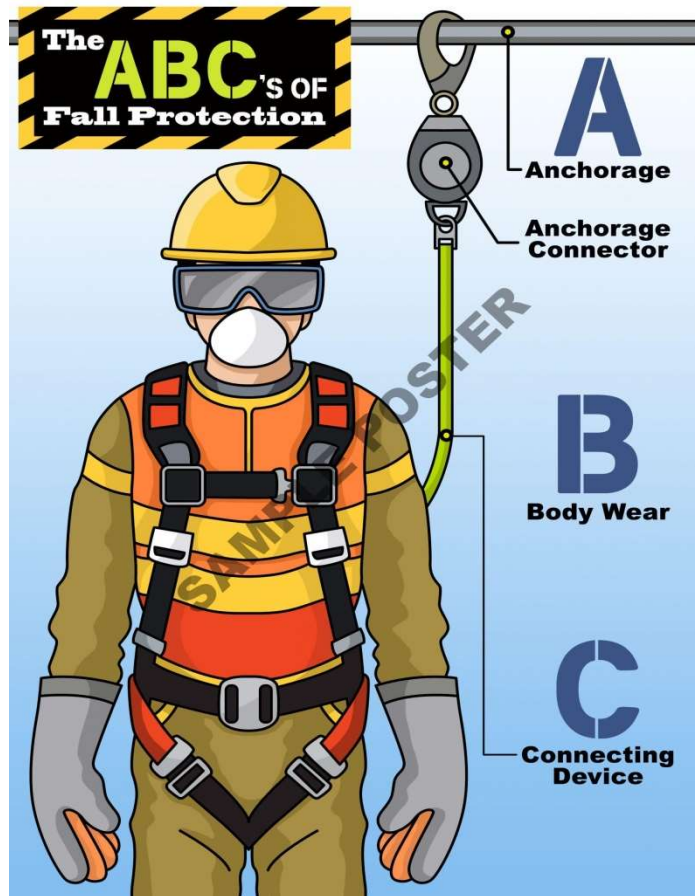



## ANNEXURE 8: ACCIDENT REPORTING

### CONSTRUCTION INCIDENT REPORT FORM

Use this form to report accidents, injuries, medical situations, criminal activities, traffic incidents, or student behavior incidents. If possible, a report should be completed within 24 hours of the event.

Date of Report: \_\_\_\_\_, 20\_\_\_\_

#### PERSON INVOLVED

Full Name: \_\_\_\_\_ Address: \_\_\_\_\_

Identification: ☐ Driver's License No. \_\_\_\_\_ ☐ Passport No. \_\_\_\_\_  
☐ Other: \_\_\_\_\_

Phone: (\_\_\_\_) \_\_\_\_-\_\_\_\_ E-Mail: \_\_\_\_\_

#### THE INCIDENT

Date of Incident: \_\_\_\_\_, 20\_\_\_\_ Time: \_\_\_\_:\_\_\_\_ ☐ AM ☐ PM

Location: \_\_\_\_\_

Describe the Incident: \_\_\_\_\_  
\_\_\_\_\_  
\_\_\_\_\_

#### INJURIES

Was anyone injured? ☐ Yes ☐ No

If yes, describe the injuries: \_\_\_\_\_  
\_\_\_\_\_  
\_\_\_\_\_

#### WITNESSES

Were there witnesses to the incident? ☐ Yes ☐ No

If yes, enter the witnesses' names and contact info: \_\_\_\_\_  
\_\_\_\_\_  
\_\_\_\_\_



## **ANNEXURE 9:**

### **COVID PROTOCOL**

**COVID is no longer considered a threat, but in the event of an increase in COVID cases or any directives or orders issued by the local or national government related to COVID, the COVID protocol will be activated.**

COVID considerations: Influx of Migrant Labour is likely as there will be a need to perform high skilled jobs which may not be available locally or even within the state. These are likely to come from other states or adjoining states or districts. Possibly 10-15 persons are required for highly skilled jobs. The remaining—semi-skilled and unskilled labor will be sourced from within the district.

At the time of labour engagement and start of work or any time during the execution of work, any directives issued by government with respect to labour, movement, labour stay at site, social distancing or any other restriction put in place to contain the spread of infectious diseases such as Covid 19.

I will monitor and ensure that contractor will follow any restriction on movement or advice on distancing as issued by government due to Covid 19 or any other infectious disease during the period of construction. I will request the details from the Contractor about the measures being taken to address the risks. This may include the following aspects as relevant

- a. Conducting pre-employment health checks
- b. Controlling entry and exit from site/workplace
- c. General hygiene
- d. Cleaning and waste disposal
- e. Adjusting work practices
- f. Reviewing accommodation arrangements, to see if they are adequate and designed to reduce contact with the community
- g. reviewing contract durations, to reduce the frequency of workers entering/exiting the site
- h. rearranging work tasks or reducing numbers on the worksite to allow social/physical distancing, or rotating workers through a 24-hour schedule
- i. providing appropriate forms of personal protective equipment
- j. Instances of spread of virus
- k. Training and communication with workers
  - Communication and contact with community
  - **IAs shall request the Contractor to convene regular meetings** with the project health and safety specialists and medical staff (and where appropriate the local health authorities), and to take their advice in designing and implementing the agreed measures.
  - **A senior person** should be identified as a focal point to deal with COVID-19 issues e.g. work supervisor or health and safety specialist



- **IAs shall request for coordination arrangements**, particularly at site where there area number of contractors and therefore (in effect) different work forces(*PIU could request the main contractor to put in place a protocol for regular meetings of the different contractors*)
- **IAs shall check with Contractors** on whether the workers are informed/ encouraged to use the existing project grievance mechanism to report concerns relating to COVID-19.



## **ANNEXURE 10:**

### **TRAFFIC MANAGEMENT PLAN (SAMPLE)**

- Kodayar Dam-I is located 47 km from Kallidaikurchi town.
- Total distance of the existing road resurfaced is 5.10 Km.
- It is proposed to transport bituminous macadam and bituminous concrete from CMP located at KadayamMadhapuram.
- Transportation of materials is intended to be done with minimum disturbance to people residing along the route.
- Materials are to be transported through 15 Nos. tippers with a truck load (of 25 MT Gross Weight, 16 m<sup>3</sup> each) which make minimum of 5 trips a day altogether.
- The road passes through ManimutharCheck post, Manjolai, NallumukkuEstates and this has to been taken into consideration while transporting the material.
- Since the materials enter into the Forest area , it is suggested that transportation of material to be done between **08:00 AM to 06.00 PM.**
- The movement of trucks are restricted during night time.

#### **Hourly traffic operations between 8.00 AM to 6.00 PM**

- Max. two forward and two return operation for 1 tipper.
- Intermediate halting point to avoid crossing of convoys.
- Average speed – 20 Km/ hour

<b>Issues</b>	<b>Solutions</b>
Damages to road	Road resurfacing at particular interval
Material spilling/ leaking/ pollution	<ul style="list-style-type: none"><li>• Maintaining sufficient freeboard</li><li>• No spill/leaking type load bodies</li><li>• Covering of material to avoid spillage</li></ul>
Operating hours inside RF	08.00 AM to 06.00 PM







## **Annexure 11**

### **SOP for Labour Camp**

- Environment and social risk of labour camp and disposal of debris has been identified as moderate.
- Further to enforce the compliance of environmental management, the contractors shall be CE responsible and liable for safety of labors and daily workers attending to the constructions iteas mandatory measures.
- The sub-project activities will require contract workers – skilled and unskilled. The unskilled workers are available locally; however, a small number of skilled work-force may come from outside the area and expected to stay at site. Influx of workers and setting up of temporary labour camp interfacing with community may increase the health risk of community.
- Migrant workers can be potential carriers of new infectious diseases not known in the area and impact the community health.
- Labour camp in vicinity of community may pose risk of unplanned waste and waste water discharge.
- Labour shall be sensitized to follow good health and hygiene practices for their as well community's health.
- Health and hygiene requirement of the labour camp shall be maintained though out the project cycle.
- Arrangements for potable water, power, community/ individual kitchen, waste management shall be done properly.
- Contractor shall ensure that safe drinking water is available for each work men. Water supply and sanitary arrangements shall be available at the labour camp.
- Separate toilets shall be made available for male and female workers staying in labour camp connected to septic tanks/ adequate waste collection and disposal arrangement. Separate, safe and easily accessible facilities for women and men in the labour Camps. (e.g., toilets should be located in separate areas, well-lit) SEA/SH is prohibited.
- Labour camp will have adequate sanitation arrangement in terms of toilet with arrangement of sewage collection and disposal. No wastewater from the camp shall



be discharged directly without any treatment in to any surface water channels or drain, which eventually joins surface water bodies.


- Waste management system shall be implemented in labour camp by providing adequate number of bins and collection system to avoid littering of wastes.
- Generated sanitary wastes from labour colony shall be disposed off properly.
- Inadequate accommodation facilities for labour, including inadequate sanitation and health facilities shall be viewed by Project Authorities and the Contractor shall be instructed to take immediate corrective actions.
- Waste generated from labour camp shall be collected after segregation, and disposed and reported in monthly report specify the quantity of wastes.
- Requirement of water and power at labour camp shall be established by contractor and discussed with Engineer in charge.
- Any access/ short cut, linking work sites and labour camp through Project Authorities shall be blocked/ fenced.
- At the time of labour engagement and start of work or anytime during the execution of work, any directives issued by government with respect to labour, movement, labour stay at site, social distancing or any other restriction shall be put in place to contain the spread of infectious disease.



## ANNEXURE12:

### Emergency Preparedness plan (EPP)

EMERGENCY PREPAREDNESS PLAN (EPP) - அமைதிப் பாதுகாப்புத் திட்டம் (EPP) - KODAYAR DAM (அமைதிப் பாதுகாப்புத் திட்டம்)					
Medical Emergency மருத்துவ அவசரம் Call medical emergency phone number: மருத்துவ அவசர தொலைபேசி எண்ணை அழைக்கவும்: Hospital No: 0422 2300600	Fire Emergency - தீ அவசரநிலை When fire is discovered: தீ கண்டுபிடிக்கப்படும் போது: Activate the nearest fire alarm	CHEMICAL SPILL - இரசாயன கசிவு When a Chemical Spill has occurred: இரசாயன கசிவு ஏற்படும் போது: Immediately notify the designated official and Emergency Coordinator.	WEATHER AND NATURAL DISASTERS - வானிலை மற்றும் இயற்கை பேரழிவுகள் Earthquake: நிலநடுக்கம்: Stay calm and await instructions from the Emergency Coordinator or the designated official.	Flood: வெள்ளம்: Be ready to evacuate as directed by the Emergency Coordinator and/or the designated official.	
மருத்துவமனை எண்: 0422 2300600	அருகில் உள்ள தீ எச்சரிக்கையை இயக்கவும்	நிவாரிக்கப்பட்ட, அங்காரி மற்றும் அவசரநிலை ஒழுக்கத்தைப் பராமருக உடனடியாகக் கொடுக்கவும்.	அமைதியாக இருங்கள் மற்றும் அவசரநிலை ஒழுக்கத்தைப் பராமருக உடனடியாகக் கொடுக்கவும்.	அவசரநிலை ஒழுக்கத்தைப் பராமருக உடனடியாகக் கொடுக்கவும்.	
Ambulance No: 108 ஆம்புலன்ஸ் எண்: 108	Notify the local Fire Department by calling No. 108 உள்ளூர் தீயணைப்புத் துறைமுகத்திற்கு தொலைபேசி 108-ஐ அழைக்கவும்.	Contain the spill with available equipment (e.g., pads, booms, absorbent powder, etc.). கிடைக்கக்கூடிய உபகரணங்களைக் கட்டுப்படுத்துதல் (எ.கா., பட்டைகள், பூம்புகள், உறிஞ்சக்கூடிய தூள் போன்றவை).	Keep away from overhead fixtures, windows, filing cabinets, and electrical power. வெள்ளிணை சாதனங்கள், துண்டங்கள், கப்பல்கள் கேபிள்கள் மற்றும் மின்சார சக்தி அகிப்பயனிலிருந்து விலகி இருங்கள்.	Follow the recommended primary or secondary evacuation routes. If outdoors: பரிந்துரைக்கப்பட்ட முதன்மை அல்லது இரண்டாம் நிலை வெளியேற்ற வழிகளைப் பின்பற்றவும். வெளியே இருக்கையில்:	
Fire Department No: 0422 23300211 தீயணைப்பு துறை எண்: 0422 23300211	If the fire alarm is not available, notify the site personnel about the fire. அவசரம் கிடைக்கவில்லை என்றால், இடத்தில் உள்ள பணியாளர்களுக்கு தொலைபேசி 108-ஐ அழைக்கவும்.	Secure the area and alert other site personnel. பகுதியைப் பாதுகாத்து மற்ற பணியாளர்களை எச்சரிக்கவும்.	Avoid people with disabilities in finding a safe place. மற்றவர்களைத் தடுக்கப் பாதுகாப்பான இடத்தைக் கண்டு கொள்ளும் சந்தர்ப்பம்.	Climb to high ground and stay there. உயரமான நிலத்தில் ஏறி அங்கேயே இருங்கள்.	
Provide First Aid Kit at site. தளத்தில் முதலுதவி கிட்டு வைக்கவும்.	The fire extinguisher is in working condition and personnel are trained to use it. தீயணைப்பூச்சி செயல்பாட்டில் பணியாளர்களுக்கு அதைப் பயன்படுத்த பயிற்சி அளிக்கப்பட்டிருக்கிறது.	Do not attempt to clean the spill unless trained to do so. கரிவைச் சுத்தம் செய்யப் பயிற்சி பெறாதவரை சுத்தம் செய்ய முயற்சிக்காதீர்கள்.	Evacuate as instructed by the Emergency Coordinator or the designated official. அவசரநிலை ஒழுக்கத்தைப் பராமருக நிவாரிக்கப்பட்ட, அங்காரி: அறிவுறுத்தலின்படி வெளியேறுவது.	Avoid walking or driving through flood water. வெள்ள நீர் தடையாகவோ வாகனம் ஏட்டுவதற்கோ தவிர்க்கவும்.	
First Aid assistance: முதலுதவி உதவி:	Leave the site using the designated escape routes. நிவாரிக்கப்பட்ட தப்பிச்சுழல் வழிகளைப் பயன்படுத்தி தப்பிச்சுழல் விலக்கு வெளியேறுவது.	Attend to injured personnel and call the medical emergency No: காயமடைந்த உபயுகத்தைப் பார்க்கு மருத்துவ அவசர எண்ணை அழைக்கவும்.		If car stalls, abandon it immediately and climb to a higher ground. கார் திறுத்தப்பட்டால், உடனடியாக அதை தகவிலிட்டு உயரமான இடத்தில் ஏறுவது.	
Stop the bleeding with firm pressure on the wounds (note: avoid contact with blood or other bodily fluids).	Escaping the area is possible by backing up to the nearest exit. அருகில் உள்ள வெளியேறுவது இடத்தில் காப்பாடு பின்பற்றி விலகி நிற்கும் அங்கு பகுதியிலிருந்து காப்பாடுவது சாத்தியமானதில்.	Deal with the spill in accordance with the instructions described in the MSDS. Small spills must be handled in a safe manner, while wearing the proper PPE. MSDS இல் விவரிக்கப்பட்ட முறை வழிமுறைகளின்படி கரிவைச் சுத்தமாக்கப்படும். சரியான PPE அணிந்திருக்கும் போது, சிறிய கரிவுகளின் பாதுகாப்பான முறைமையில் கையாள வேண்டும்.			
Clear the air passages in case of choking.					
When personnel exposed to hazardous materials, consult the Material Safety Data Sheet (MSDS).					
When personnel exposed to hazardous materials, consult the Material Safety Data Sheet (MSDS).					





### ANNEXURE13:

**Fire Fighting Appliances Types of Extinguishers suited for the three classes of fire is as follows:**

Type of extinguishers	Class A	Class B	Class C
Carbon-di-oxide	Suitable for small surface fire only.	Suitable. Does not leave residue or affect equipment or food or food stuff.	Suitable, non-conductor and does not damage equipment.
Dry Chemical	Suitable for small surface fire only	Suitable, Chemical releases smothering gas and fog and shields operator from heat.	Suitable, Chemical is a non-conductor fog or dry chemical shields operator from heat.
Foam	Suitable, has both smothering and wetting action	Suitable, smothering blanket does not dissipate, floats on top of spilled liquid.	Unsuitable, foam being a conductor should not be used on live equipment.
Water	Suitable, Water saturates material and prevents re-kindling	Unsuitable, water will spread and not put it out.	Unsuitable, water being conductor should not be used on live electrical equipment.
Vaporizing liquid	Suitable for small surface fire only	Suitable, releases heavy smothering gas on fire.	Suitable, non-conductor and will not damage equipment.

### Fire and Fire Protection:

Insulation Class	Types of Fire	CO <sub>2</sub>	Dry Chemical	Foam	Water
Class A	Paper, Wood, cloth excelsior, Rubbish etc., where quenching fires and cooling affects only of water is required	Small surface fire only.	Small Surfaces fire only.	Yes. Foam has both smothering and wetting action and excellent.	Yes. Water separate the materials prevent radicals.



Class B	Burning liquids (Gasoline, oils, Paints, Coating fats etc.,) Where smoothening action is required.	Yes. CO <sub>2</sub> leaves no residue does not affect equipment.	Yes. Chemical releases smoothening gas or fires log or dry chemicals shields operator from heat.	Yes. Smoothening blanket does not dissipate floats on top of spilled.	No. water will spread, not put it out.
Class C	Fire in live Electrical equipment (Motor, switches appliances etc.,) where a non-conducting extinguisher agent is required.	Yes. CO <sub>2</sub> is a non-conductor leaves no residue, will not damage equipment	Yes. Chemical Is a non-conductor fog or dry chemical shields operator from heat.	No. foam is a conductor and should not be used on line electrical equipment.	No. Water is a conductor should not be used on line electrical equipment.
